Moss

Sign of Quality

## Atlanta Fulton County Public Library System – Alpharetta Public Branch

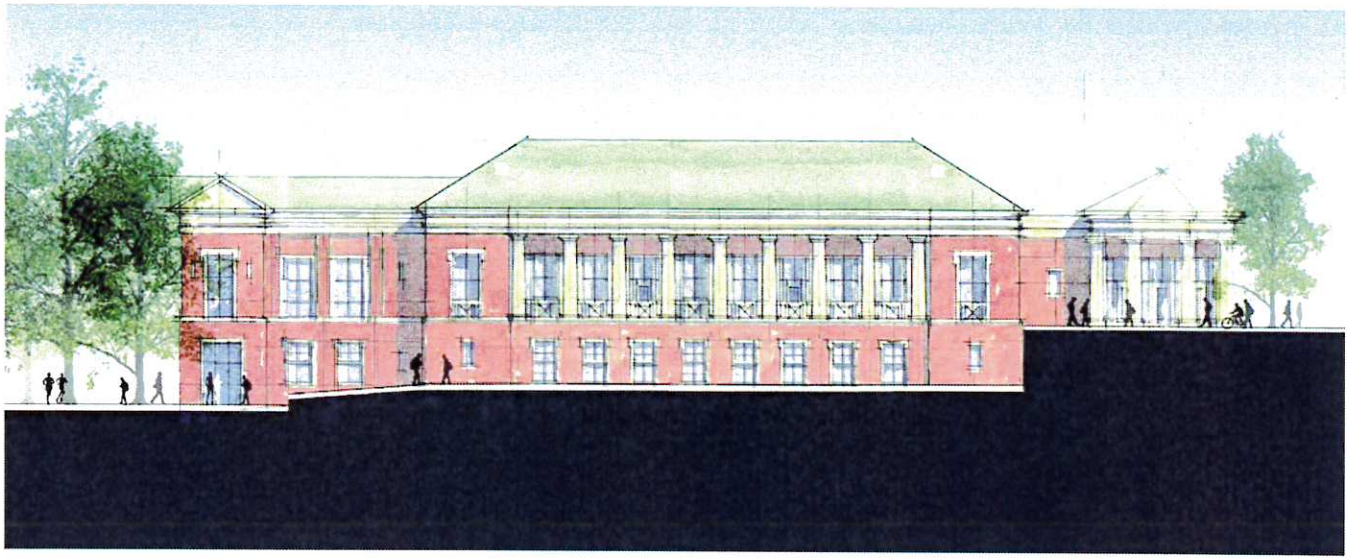

# Addendum/Bulletin #2
# 6/3/14

FULTON COUNTY

COOPER CARRY
The Center for Connective Architecture

atlanta-fulton public library system

2675 Paces Ferry Road, SE | Suite 200 | Atlanta, GA 30339

Phone: 770-436-0000 | Fax: 770-436-6000

# Items

**Item 1) RFI #14 – Landscape Stepping Stones (RFI Attached)**

**Item 2) RFI Audience Seating**

- Is cast iron an acceptable substitute? Is steel an acceptable substitute? **Answer: Yes**
- The specifications require the chair to pass Cal 133 testing. Is this required? **Answer: No, Cal 133 standard is not required.**

**Item 3) Site Furnishing Products:**

- **8' Bench** - Robinson Iron - 8' Long Expo / Hoop Style Bench with Clear White Oak Slats
- **Bike Rack** - Dero Round Bike Rack
- **Trash Receptacle -** Kings River Casting - Square Iron Valley Trash Receptacle - Surface-Mount - Features vertical flat steel bars and decorative rings at the top - Includes a Rain Bonnet and a 32 Gallon Plastic Liner Can
- **4' Bench -** Country Casual - 4' Long Teak Monarch Bench - Portable

atlanta-fulton public library system

*Take your dreams off the shelf.™*

# Request For Information

**Project** [L001] - Alpharetta Branch Library **View Date** 5/7/2014

Moss & Associates formerly known as P.R.B.C., Inc.
Central Library,
One Margaret Mitchell Sq.
6th floor
Atlanta, GA 30303

**RFI No.** 00014

| | | | |
|---|---|---|---|
| **Primary Responder** | | **Date** | 5/7/2014 |
| **CC** | | **Status** | |
| **From** | Andrew Virga<br>Moss & Associates formerly known as P.R.B.C., Inc. | **Resolved Date** | |
| | | **Reason for Request** | Insufficient Information |
| | | **Action Requested** | Clarification |
| | | **Probable Cost Effect** | None |
| | | **Probable Time Effect** | |
| | | **Priority** | Medium |
| | | **Response Due** | 5/14/2014 |

**Subject** Stepping Stone and Pebble Clarification
**Drawing No.** L1.01 **Detail No.** P-105 & P-106
**CSI Code** **Other Ref. No.**

**Information Requested**

-Please include an estimated quantity, in square footage or unit count, for 2" Crab Orchard Stepping Stone (P-105) and Black Mexican Beach Pebble (P-106)

-Please indicate percentage of each stone size for 2" Crab Orchard Stepping Stone (P-105)

-Please indicate if landscaping fabric is required underneath 2" Crab Orchard Stepping Stone (P-105) or Black Mexican Beach Pebble (P-106)

**Recommendation**

**Response Information**

| Responder | Date | Response |
|---|---|---|

Unit count of crab orchard stepping stone - 375 stepping stones. 25% 30" - 25% 24" - 25% 18" - 25% 12"
No filter fabric under stepping stones.
140 sq ft of black mexican beach pebbles, 3" deep (to insure no fabric or dirt shows below) with landscape fabric.
Stephen Busch/Cooper Carry 5-8-2014
