East Roswell Library

Atlanta-Fulton Public Library Capital Improvement Plan

Bid Package No. 2.1 – Sitework & Utilities

Ajax Project No. 201209

April 8, 2013

FULTON COUNTY

Ajax BUILDING CORPORATION OF GEORGIA

atlanta-fulton public library system

JOB NAME: East Roswell Library
JOB NO.: 201209

TABLE OF CONTENTS
Bid Package No. 2.1 - Sitework & Utilities

	Section		Pages
I.	INVITATION TO BIDDERS		
	(Project-specific) Notice to Bidders		1
	(General) Instructions to Bidders		8
II.	SCOPE OF WORK		
	Scope of Work	(Contract Schedule "A")	12
	Insurance Requirements	(Contract Attachment "C")	1
III.	PROPOSAL FORM		
	Proposal Form		4
	Bid Proposal Affidavit		1
IV.	SCHEDULE		
	Project CPM Schedule		5
V.	SUBCONTRACT AGREEMENT		
	Subcontract		14

Date **April 9, 2013** **NOTICE TO BIDDERS**

Bids for furnishing all labor and material and performing all work necessary and incidental to the completion of

Bid Group	Bid Package No. & Description		Pre-Bid Date / Time	Bid Date / Time
A	2.1	Sitework & Utilities	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
A	3.1	Concrete	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
A	4.1	Masonry	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
A	5.1	Structural & Miscellaneous Metals	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
B	7.1	Roofing	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
B	8.2	Glass, Glazing, Storefront, & Sun Control	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
B	9.1	Drywall, Framing & Stucco	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
B	23.1	HVAC & Controls	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm
B	26.1	Electrical	04/**18**/2013, 2:00 pm	**05/02**/2013, 2:00 pm

for East Roswell Library will be received by Fulton County Department of Purchasing on behalf of Ajax Building Corporation of Georgia until the above referenced dates and times.

Ajax Building Corporation of Georgia will be the point of contact for this bid package, except for bid receipt.
5950 Shiloh Road East, Suite S, Alpharetta, GA 30005
Phone: 770-952-7422; Fax: 770-952-7459;
Email: Rebecca Bailey (rebecca@ajaxbuilding.com), Ed Hill (ehill@ajaxbuilding.com).

Mailed or Hand Delivered Bids

Fulton County Department of Purchasing and Contract Compliance
c/o Ajax Building Corporation – East Roswell Library, Fulton County Public Safety Building
130 Peachtree Street, S.W., Suite 1168, Atlanta GA 30303

E-mailed or Faxed Bids
Attn: Linda Walton
Email: Linda.Walton@fultoncountyga.gov (copy to: rebecca@ajaxbuilding.com)
Fax #: 404-335-5029

The Contract Documents, as defined in Subcontract Agreement form, may be examined at the office of Ajax Building Corporation of Georgia, 5950 Shiloh Road East, Suite S, Alpharetta, GA 30005.

Bid Documents
Bid Documents will be provided electronically. Bidders may obtain Bid Documents by accessing Ajax Building Corporation of Georgia's FTP site as indicated below. Plans and Specs are available now, and Bid Packages are scheduled for April 4, 2013.

FTP Site Address: **ftp://ftp.ajaxbuilding.com/**
Web Access Address: **http://ftp.ajaxbuilding.com/**
Subcontractor Username: eastroswellsub
Subcontractor Password: 201209sub

Bid Documents may also be reviewed at the office of Ajax Building Corporation of Georgia, or through:

- McGraw-Hill/Dodge, Reed Construction Data, iSqFt®, and LDI-Line *(purchase required).*
- The project will also be listed on the Fulton County Bid Board, though Plans/Specs will not be posted there.

No bids may be withdrawn after the scheduled closing time for receipt of same for a period of ninety (90) days.

Proposals shall be plainly marked, "Bid", with name of project, bid package number and description, name and address of bidder, time and date due. Dates are subject to change. Notice will be given to Pre-Qualified bidders.

The Construction Manager reserves the right to reject any and all bids received and to waive any and all informalities or irregularities in regard thereto.

Pre-Bid Conferences will be held at **East Roswell Park Community Room, 9000 Fouts Road, Roswell, GA 30076** on the above listed dates and times. Pre-Bid Conferences are not mandatory.

INSTRUCTION TO BIDDERS

1. GENERAL

1.1 Ajax Building Corporation, Construction Manager, will receive proposals for furnishing all labor and material and performing all work necessary and incidental to the completion of Bid Package No. 2.1, entitled Sitework & Utilities, for East Roswell Library. Proposals will be accepted by Fulton County Department of Purchasing on behalf of Ajax Building Corporation at 130 Peachtree Street, S.W., Suite 1168, Atlanta, GA 30303 until 2:00 p.m. Local Time, on the date listed in the Notice to Bidders. The contract for Work shall be between the Subcontractor and Ajax Building Corporation. The Scope of Work is described in the Form of Agreement between Construction Manager and Subcontractor.

1.2 The Construction Manager reserves the right to reject any or all bids, accept bids in any order or combination, make modifications to the work after bidding, and waive any informalities or irregularities in bids if it is deemed in the Owner's best interest to do so. All bids are subject to the review and approval by the Owner, or their designated representative.

1.3 Conflict of Interest: All bidders must disclose - with their bid - the name of any officer, director, or agent who is also an employee of the Owner. Further, all bidders must disclose the name of any Owner employee who owns, directly or indirectly, an interest of ten percent (10%) or more in the bidder's firm or any of its branches.

1.4 The Construction Manager is Ajax Building Corporation, 5950 Shiloh Road East, Suite S, Alpharetta, GA 30005. The Construction Manager reserves the right to submit a sealed bid, or not to submit, for any bid package for this Project.

1.5 The Project Architect is Khafra Engineering Consultants, Inc. The Library Architect is Holzheimer Bolok + Meehan (HBM) Architects. The Civil Engineer is Long Engineering, Inc. The Structural Engineer is Khafra Engineering Consultants, Inc. The Mechanical Engineer is KAI Design&Build. The Electrical Engineer is Khafra Engineering Consultants, Inc.

1.6 The Owner is Fulton County, a political subdivision of the State of Georgia.

2. BIDS

2.1 All bids must be submitted on the Proposal Form supplied by Construction Manager, and shall be subject to all requirements of the Contract Documents. All bids must be regular in every respect; all applicable spaces shall be filled in, and no interlineations, exclusions or special conditions shall be made or included in the Form by the bidder. Conditional bids will not be accepted, nor will oral, or telephone bids. Erasures or other changes in the bids must be explained or noted over the signature of the bidder.

2.2 Each bidder, by making this bid, represents that:

A. Bidder has read and understands the Bidding Documents and this bid is made in accordance therewith.

B. Bidder has visited the site and has familiarized themselves with the conditions under which the Work is to be performed.

C. This bid is based upon the materials, systems and equipment described or named in the Bidding Documents without exception.

2.3 Mailed or Hand-delivered Proposals shall be sealed and plainly marked, "Bid", with name of project, bid package number and description, name and address of bidder, time and date due. If the bid is sent by mail, the sealed envelope shall be enclosed in a separate mailing envelope with the notation "BID PACKAGE NO. 2.1 ENCLOSED" on the face thereof, and addressed to the Construction Manager at the address

indicated in the Notice to Bidders. To be considered, each envelope shall contain an original of the following:

A. Proposal Form (completed and executed).

B. Bid Proposal Affidavit.

2.4 Each copy of the bid proposal shall include the legal name of bidder and a statement whether bidder is a partnership, a joint venture, a corporation or any other legal entity, and each copy shall be signed by the person or persons legally authorized to bind the bidder to a contract. A bid by a corporation shall give the State of Incorporation, and shall have the corporation's seal applied to it.

3. MODIFICATION OR WITHDRAWAL OF BIDS

3.1 Bids may be withdrawn or modified on written or telegraphic request dispatched by the bidder and received by Fulton County Department of Purchasing on behalf of the Construction Manager prior to the time for receipt of bids, provided that written confirmation of any telegraphic withdrawal under the signature of the bidder shall be placed in the mail with the postmark prior to the time set for receipt of bids. It shall be worded so as not to reveal the amount of the original bids.

3.2 Negligence on the part of the bidder in preparing his bid confers no right for the withdrawal of the bid after it has been opened.

4. PREQUALIFICATIONS OF BIDDERS

4.1 The agreement will only be entered into with responsible subcontractors found to be satisfactory to the Owner and the Construction Manager, qualified by experience and in a financial position to do the work specified. The bidder must, upon request, be able to prove his financial ability to carry on the work until such time as he received his first payment, and to finance the work between payments until the contract is completed and accepted.

4.2 More than one bid from an individual, firm, partnership, corporation or association under the same or different names will not be considered. If more than one such bid is received, only the lowest conforming bid will be considered.

5. BIDDING DOCUMENTS

5.1 Contract Documents are as enumerated in the Subcontract Agreement. Each bidder shall promptly review all Contract Documents to assure completeness. If, for any reason, an item is missing from the transmitted list, he shall so notify the Construction Manager in writing, who will assist in his receiving missing item(s). Missing items shall not constitute grounds for modification of the contract.

5.2 Any addenda issued during the bidding period will be posted to Ajax's FTP site. Email notification of posting will be issued ONLY to the bidders and suppliers to whom access to Contract Documents have been provided by Ajax directly.

5.3 No partial sets of drawings and specifications will be issued.

6. INSPECTION OF SITE

6.1 Each bidder shall visit the site(s) of the proposed work and fully acquaint himself with the existing conditions there relating to construction and labor, and shall fully inform himself as to the facilities involved, the difficulties, restrictions and logical extensions of Scope attending the performance of the contract. The bidder should thoroughly examine and familiarize himself with the drawings, technical specifications and all other Contract Documents. The subcontractor, by the execution of the contract, shall in no way be relieved of any obligation under it due to his failure to receive or examine any form, or legal

instrument, or to visit the site and inform himself thoroughly regarding any and all conditions and requirements that may in any manner affect the work to be performed under the contract. Lack of knowledge on the part of the Bidder will in no way relieve him of the obligations and responsibilities assumed under the contract.

7. INTERPRETATIONS AND ADDENDA

7.1 Bidders shall promptly notify the Construction Manager of any ambiguity, inconsistency or error which they may discover upon examination of the Contract Documents for each portion of the Project or the site and local conditions. No oral interpretation will be made to any bidder as to the meaning of the Contract Document or any part thereof. Every request for such an interpretation shall be made in writing to Ajax Building Corporation, 5950 Shiloh Road East, Suite S, Alpharetta, GA 30005, Attn: Rebecca Bailey (rebecca@ajaxbuilding.com).

7.2 Every interpretation made to a bidder will be in the form of an Addendum to the Contract Documents prepared by the Construction Manager with assistance from the Architect (when required) and, when issued, will be on file in all of the offices to which the Contract Documents have been issued. It shall be the bidder's responsibility to obtain all Addenda issued. All such Addenda shall be listed on the Bid Form in the space provided and shall become part of the contract. Each bidder shall be bound by such Addenda, whether or not received by the bidder. Only a written, or telegraphic interpretation or correction by Addendum, or Supplement issued by Construction Manager will be binding.

8. POST BID INFORMATION

8.1 Unless waived by the Owner, the successful bidder for each portion of the Project shall, within ten (10) days of notification of selection, submit the following information to the Construction Manager:

A. Percentage of work to be performed by bidder with his own forces.

B. Proprietary names of the suppliers or principal items, or systems of material and equipment proposed for the work.

C. List of all sub-subcontractors who will perform work for the bidder and the percentage of work to be performed by each sub-trade contractor.

D. Insurance Certificates.

E. Executed Subcontract. (Within seven (7) days)

F. A complete material cost breakdown for Owner's use.

G. Submittal and Schedule Outline.

H. Schedule of Values in a form acceptable to Construction Manager. Schedule of Values shall be broken down by each building or facility on site. For trades with work both inside and outside of a structure, work and costs associated with the structure shall stop five (5) feet outside the building line. The remainder of the work outside the structure (if any) will be described as "site".

8.2 Prior to the award of contract, Construction Manager will notify the bidder if he, or the Owner, after due investigation, has reasonable and substantial objection to any person or organization submitted. If such an objection is expressed and if the Construction Manager or the Owner refuses in writing to accept such person, or organization, the bidder may submit an acceptable substitute sub-subcontractor with an increase or decrease in his bid price to cover the difference in cost occasioned by such substitution. The Owner or Construction Manager may, at his discretion, accept the revised bid price or he may disqualify the bidder.

8.3 Sub-subcontractors and other persons and organizations proposed by the bidder and accepted by the Construction Manager and the Owner, must be used on the work for which they were proposed and accepted, and shall not be changed except with the written approval of the Construction Manager and the Owner.

8.4 The Owner, and/or the Construction Manager, reserves the right to remove, or cause to be removed from the Project, any employee of the subcontractor or their sub-subcontractors, whenever it deems, in its sole discretion, such action to be in the best interest of the Project. Such removal of undesirable personnel will in no way change or reduce the obligations of the subcontractor.

9. FORM OF CONTRACT

9.1 The form of Agreement between subcontractor and the Construction Manager is enclosed in the Bid Package Documents, copies of contract attachments are available upon request. **The bidder shall take no exception to the terms and conditions of this Agreement.**

9.2 Upon execution of the Subcontract Agreement by Construction Manager and successful bidder, the bidder will hereinafter be called the subcontractor and the Construction Manager may also be referenced as the Contractor.

10. AWARD OF CONTRACTS

10.1 It is intended that separate contracts shall be awarded for each bid package and that the work start as soon after award as possible; but bids may be held for a period not to exceed (90) days from the bid opening dates, and no bidder may withdraw his bid during this period.

10.2 Award of contracts for each portion of the Project will be made to the best and most responsive qualified bidder.

11. SUBSTITUTIONS/APPROVED EQUAL MATERIAL OR EQUIPMENT

11.1 Requests for substitutions will be considered only after receipt of the bid. No substitution will be considered unless written request for approval has been submitted by the bidder to the Construction Manager at bid time. Request shall be in the form of an alternate to the base bid and shall be so stated on the proposal form.

11.2 Materials, products and equipment described or named in the Bid Documents establish a standard or required function, dimension, appearance and quality to be met by any proposed substitution. Each bid shall be based upon the materials and equipment described, or named in the Bid Documents. Where systems or products are designated in the Specifications or on the Drawings by reference to trade names, manufacturer's names, model numbers, catalog numbers, etc., bids shall be based on the specific system or products so designated, and the contract will be awarded on that basis, or substitutions/approved equal material, or equipment approved by Addenda.

11.3 Requests for substitutions /approved equal material or equipment will be entertained where the bidder considers that the proposed substitute will offer better service, more advantageous delivery date, or lesser price, with credit to the Owner, without sacrificing quality, appearance or function. It shall be understood that approval, or rejection is in no way an endorsement, or derogation of the product.

11.4 Each substitution /approved equal material or equipment request shall include an electronic copy of submittal data and six (6) complete sets of physical samples if applicable; contain the name of the material or equipment for which it is to be substituted, drawings, cuts, performance and test data, and any other information necessary for evaluation. A statement setting forth any changes in other materials, equipment or work that incorporation of the substitute would require, shall be included. The burden of proof of the merit of the proposed substitute is upon the proposed. The Architect/Engineer's decision, made through the Construction Manager, of approval, or disapproval of a proposed substitution shall be final.

11.5 If approval is made of any proposed substitution /approved equal material, or equipment, such approval will be set forth in a written, or telegraphic Addendum to the Contract Documents; issued by Construction Manager. Bidders shall not rely upon approvals made in any other manner.

12. SCHEDULES

12.1 The Project will be scheduled by the Critical Path Method by the Construction Manager. A detailed CPM Schedule is included in this Bid Package and is part of the contract Documents. The successful subcontractor will be required to furnish, within ten (10) days after notification of selection, information necessary to bring about a construction and purchasing schedule allowing for completion of the Project within the time allowed on the Master Project CPM Schedule. Information shall be in a form acceptable to the Construction Manager. The Construction Manager will require the subcontractor to review the Construction Manager's CPM Schedule, at intervals required by the progress of the Work.

12.2 The progress of the subcontractor is critical to the progress of the Project. Therefore, the schedule shown in the contract Scope of Work must be met. Failure to maintain this schedule will cause the subcontractor to be subject to assessment of milestone damages.

13. PERMITS

13.1 Unless otherwise provided in the Contract Documents, the Construction Manager shall secure and pay for the building permit and impact fees. The subcontractor shall secure and pay for all other permits, (i.e. plumbing, mechanical, electrical, etc.) governmental fees, licenses and inspections necessary for the proper execution and completion of the Work.

14. ENGINEERING

14.1 Each bidder must include in his proposal all costs for verifying the suitability of the Work by others which affects the subcontractor's work, and perform all engineering, and surveying and field measurements which may be required to complete the Work.

14.2 Basic reference points and bench marks will be provided by Construction Manager. Subsequent surveying and field measurements from these points will be the responsibility of each subcontractor.

15. INSURANCE

15.1 The successful bidder shall provide General Liability Insurance, Automobile Liability Insurance, and Worker's Compensation Insurance as outlined in Attachment C. Certificates of Insurance shall be on a form acceptable to the Construction Manager and shall provide an unconditional thirty (30) days written notice of cancellation. Subcontractors may be enrolled in an Owner-Controlled Insurance Program (OCIP) for General Liability Insurance at a later date, program documentation is available upon request.

16. UNIT PRICES

16.1 Unit prices, if requested in the Bid Documents, shall be used, where applicable, to pay for completed work contained in the Contract Documents, or to make adjustments to the cost of the Work of the contract due to changes to the Work required by the drawings and specifications. The prices shall be predicated upon the materials, methods and standards of quality set forth in the Contract Documents. Unit prices submitted shall be reasonable within the range of the current pricing in the region for complete in-place work. Unit prices shall include all costs for overhead, profit, all applicable federal, state, municipal or local taxes, labor material, equipment and any other incidentals related to completion of the work. Unit prices for deletions shall be the same as unit prices for additions. The selected bidder for each bid package shall hold his unit prices for the life of the subcontract agreement. Unit prices will not be a consideration in selecting the low bidder or as a basis of award of contract. The Owner and Construction Manager reserve their right to reject any unit price if considered excessive or unreasonable or to accept any and all such unit prices which may

be considered fair and reasonable.

17. ALTERNATES

17.1 Alternates, if requested, are to enable the Owner to compare total costs where alternate materials and methods might be used. Alternates will be described on the drawings and in Schedule "A" of the Subcontract Agreement. Alternate prices are “all inclusive” and include all overhead and profit.

A. The successful bidder shall not modify, withdraw or cancel any of the alternate bids, for 120 days (unless a longer duration is identified in a specific alternate) after the date of Notice of Award.

B. Subcontractor shall be responsible for any changes in the Work affected by acceptance of these alternates. Claims for extras resulting from changes caused by the alternates will not be considered.

C. The Owner's selection of any alternate does not relieve the subcontractors of timely completion of the Project within the time periods indicated.

17.2 Materials and methods to be used in the Base Bid and in the Alternates are described in the contract documents.

18. RIGHT TO WORK

18.1 Consideration and acceptance of contracts shall be without regard as to whether or not the subcontractors, or its employees are members of a labor union or labor organization. It shall not be a condition of making any bid or proposal, or for performance of work, that any person be a member of a labor union or labor organization.

19. MATERIAL, SUPPLIES & EQUIPMENT - OWNER'S SALES TAX EXEMPTIONS

19.1 **Bidder shall include Georgia State and other applicable sales taxes** for all material, supplies and equipment included in the Work.

19.2 If the Owner is tax exempt and exercises his right to purchase directly various construction materials, supplies and equipment that may be a part of this contract, then the Construction Manager will act as the Purchasing Agent for the Owner. The Owner will, via his purchase orders, purchase the materials, and each subcontractor shall assist the Construction Manager in the preparation of purchase orders. The materials shall be purchased from the vendors/suppliers selected by the subcontractor, for the prices negotiated by the subcontractor.

19.3 The contract amount shall be reduced by the net, undiscounted amount of the purchase orders, plus all sales taxes. Issuance of the purchase orders by the Owner shall not relieve the subcontractor of any of his responsibilities regarding material purchases, or installation, with the exception of the payments for the materials so purchased. Subcontractor shall remain fully responsible for coordination, correct quantities ordered, submittals, protection, storage, scheduling, shipping, security, expediting, receiving, installation, cleaning and all applicable warranties.

20. OTHER OWNER-FURNISHED EQUIPMENT

20.1 Certain items scheduled in the Contract Documents are to be furnished directly by the Owner, to the project site unless otherwise indicated, and are to be received and installed by the subcontractor.

20.2 Within fifteen (15) calendar days after receipt of notification of selection for the award of a contract for the Work, the subcontractor shall submit to the Construction Manager, a schedule, giving desired dates for delivery of Owner-furnished items. Approved dates of delivery shall be confirmed to the Construction Manager thirty (30) days prior to delivery, by subcontractor. Subcontractor shall accept delivery on the

established dates or be responsible for any damage resulting from his failure to take delivery of the shipment on established dates. Promptly upon delivery, the subcontractor, jointly with the Construction Manager, shall inspect the materials or equipment for possible shortage or damage in transit. If shortage or damage is found, subcontractor shall follow the instructions of the bill of lading for reporting to the carrier. Subcontractor shall submit a complete receiving report acceptable to the Construction Manager.

20.3 Subcontractor shall receive, store, protect, secure and unload the items, sign for, provide additional transportation required, uncrate, assemble, locate in place and install, or connect ready for operation and use and clean for final inspection. For details of construction and installation of each item, see drawings and standard details. Installation, or connection shall be in accordance with specifications for such work, including fitting to adjacent work and any additional labor and material required. All materials/equipment received shall be properly and legibly listed and signed for on Owner's "Receiving Ticket" form, as well as Shipper's packing slip. The receiving person's name and company must be legibly shown on all such documents.

21. SEQUENCE OF CONSTRUCTION

The sequence of construction shall be as outlined in the CPM Schedule.

22. APPRENTICE LABOR REQUIREMENTS

This project shall be subject to apprentice labor requirements as enumerated in Georgia Statutes. The Subcontractor is hereby instructed to become familiar with the conditions contained in the aforementioned documents and to abide by them under penalty of law.

23. DISQUALIFICATION OF BIDDERS

Any or all Proposals may be rejected if there is reason to believe that collusion exists among the Bidders. Participants in such collusion will not be considered in future Proposals for the same Work. Proposals in which prices are obviously unbalanced may be rejected by the Owner.

Falsification of any entry made on a Bidder’s Prequalification Statement or Proposal will be deemed a material irregularity and will be grounds for rejection.

24. DRUG FREE WORKPLACE CERTIFICATION

Bidders shall provide evidence for certification of a drug free workplace. Preference may be given to businesses with drug-free workplace programs whenever two or more bids which are equal with respect to price, quality, service and location are received for the procurement of a Subcontract for this project.

25. BIDDER PREFERENCES

If all other factors are equal, preference will be given to a Georgia resident Bidder over an out-of-state resident. If all Bidders are Georgia residents, a Fulton County Bidder will receive preference; if there is no Fulton County Bidder, preference will be given to the Bidder closest to Fulton County. If all Bidders reside out-of-state or all reside within Fulton County, preference shall be given to the Bidder who certifies it has implemented a drug-free workplace program. In order to receive preference, a signed certification of compliance must be submitted with the bid response. If all bids or no bids include a certificate of compliance, the tie will be broken by a coin flip in the presence of witnesses.

26. GEORGIA PRODUCTS AND LABOR

In accordance with applicable Georgia Statutes, on public building Contracts, Georgia products and labor shall be used wherever price and quality are equal, subject to considerations set forth in the Statutes relating to comparisons of quality and fitness or materials and equipment as well as qualifications, character, and responsibility of contractors and builders proposed for employment.

27. MINORITY, WOMEN & DISADVANTAGED BUSINESS ENTERPRISE (MWDBE) PARTICIPATION

27.1 AJAX COMMITMENT

As a matter of policy, Ajax Building Corporation of Georgia is committed to providing opportunities for all businesses, including small, minority, women, and disadvantaged business enterprises, in the procurement of goods and services and construction related subcontracting. Ajax Building Corporation of Georgia firmly believes that in our free enterprise system, every attempt must be made to fully utilize all of our resources, human as well as material. Our commitment is to promote and maximize the opportunities for MWDBE participation on our projects through the development of mutually beneficial business relationships with the various organizations, subcontractors, suppliers and vendors. Upon request, Ajax Building Corporation of Georgia will make available our talent, knowledge and resources to assist in the development of these business relationships.

27.2 PROJECT REQUIREMENTS AND GOALS

There are no minimum requirements or stated goals for Minority, Women and Disadvantaged Business Enterprise (MWDBE) participation for this project, although Bidders, to the extent consistent with quality, price, risk, and other lawful and relevant considerations, are encouraged to include and/or provide opportunities for MWDBE participation and shall exercise good faith efforts to maximize MWDBE participation for the Work of this Bid Package. MWDBE participation will not be used by the Construction Manager or Owner as a basis of award.

28. WORKER SCREENING

There will be a Worker Screening program in place for this jobsite which all subcontractors, sub-subcontractors, suppliers, consultants, and other firms supplying materials, equipment, or labor, or performing services or work on the project will be required to adhere to. This includes participation in the U.S. Department of Homeland Security E-Verify Program.

29. JOBSITE PROCEDURES

29.1 Each Subcontractor shall be responsible for providing their own storage sheds, storage containers, gang boxes, etc. needed for his work. The Subcontractor shall be responsible in all respects for the contents stored therein. Construction Manager approval shall be obtained for any storage and staging areas prior to the Subcontractor mobilization. No materials or equipment shall be stored within the building unless authorized in writing by the Construction Manager.

29.2 Drinking water and ice shall be provided by each Subcontractor. All utilities, related infrastructure, connections, fees, etc. for Subcontractor office trailers (if such trailers are approved by the Construction Manager) will be the responsibility of the Subcontractor. Any special utility requirements (i.e. utility requirements other than standard 120V receptacles and standard ¾” hose bibbs) required in the performance of the Subcontractor’s work shall be the responsibility of the Subcontractor. Temporary heat and/or ventilation required to properly execute the work will be the responsibility of the Subcontractor.

29.3 No signs shall be posted by any Subcontractors unless approved in writing by the Construction Manager.

29.4 The Construction Manager will determine the areas where employees may park. Unauthorized vehicles parked on-site will be towed at the Owner's expense. All construction personnel shall enter and exit the construction site through the construction entrances designated by the Construction Manager.

29.5 Dumpsters will be provided by the Construction Manager for construction debris only. The dumpster location(s) will be designated by the Construction Manager. It is the responsibility of the Subcontractor to remove construction debris from the building or site and to place the construction debris into the dumpsters. The following materials will not be allowed in dumpsters and it is this Subcontractor’s responsibility to dispose of these items in a lawful manner: Hazardous materials of any kind, Buckets of any size, Carpet remnants, Household trash, Perishable items, Liquids, Appliances, and Computers.

A. DEFINITION, CORRELATION AND INTENT

The following requirements form a part of the Contract Documents for, and refer solely to, the Work of the above entitled Bid Package. All information contained herein is provided for the purpose of defining and describing the work which shall be included in the Scope of Work of this Bid Package and to identify certain specific information which bidders will be required to furnish as a part of their Proposal for this Work as described in the Contract Documents. It is intended that the requirements of the Section shall be complementary to, and shall be correlated with the requirements of all other Contract Documents referenced herein and made part of the Contract.

The organization of the specifications into divisions, sections, and articles and the arrangements of the drawings shall not control the Construction Manager in dividing the work among Subcontractors or establishing the extent of the work to be performed by any Trade.

B. SCOPE OF WORK

B.1 Reference is made to the following Specification Sections, which relate to the Scope of Work, but is in no way intended to limit or alter the intent of the Contract Documents.

Division 1	General Requirements
---	All Sections
018113	Sustainable Design Requirements – LEED for New Construction and Major Renovations

Division 22	Plumbing
221116	Domestic Water Piping
221313	Facility Sanitary Sewers

Division 31	Earthwork
311000	Site Clearing
312000	Earthmoving

Division 32	Exterior Improvements
321216	Asphalt Paving
321313	Concrete Paving
323223	Modular Concrete Retaining Wall

Division 34	Utilities
334100	Storm Utility Drainage Piping

Geotechnical Report
Subsurface Exploration and Geotechnical Engineering Evaluation for the East Roswell Branch Library from Willmer Engineering, Inc. dated August 03, 2012

B.2 This work of this Bid Package includes, but is not limited to:

1. All site work and utilities in strict accordance with the Contract Documents, including:
   A. Erosion control and environmental protection throughout all phases.
   B. Demolition, clearing and grubbing.
   C. Relocation and removal of existing site utilities.
   D. Excavation, backfill and grading.
   E. Surcharging and proof-rolling of specified areas.
   F. Site water systems.
   G. Site fire systems.
   H. Sanitary sewer systems.
   I. Site storm water system.
   J. Modular Concrete retaining walls.
   K. Asphalt and concrete paving.
   L. Removal and replacement of existing improvements (as shown on the Contract Documents and/or required in the performance of your work).

2. Erosion Control and Environmental Protection:
   A. This Subcontractor will be responsible for securing all approvals and for the implementation of all erosion control and environmental protection required by federal, state and local agencies having jurisdiction over the project.
      1. This Subcontractor shall have all erosion control and environmental protection requirements in place prior to the start of any sitework.
      2. Include all fees, notices, inspections, reports and other documentation required for complete compliance.
      3. Any enforcement action by the governing authority will be this Subcontractor's responsibility.
      4. Any action by another party having the potential to create a situation of non-compliance should be reported in writing to the Construction Manager for action on the part of the Construction Manager to assist in preventing non-compliance or restoring the site into compliance.
      5. All costs for establishing, maintaining or restoring compliance will be this Subcontractor's responsibility unless this Subcontractor provides the Construction Manager with sufficient documentation to hold another party responsible. The burden of proof lies with this Subcontractor.
   B. Prior to the start of work, install all temporary silt fencing around the perimeter of the construction site and install all tree protection as required and/or indicated in the Contract Documents. Silt fencing shall consist of posts, hog wire fencing, filter fabric and hay bales.
   C. Install, maintain and remove from the site when no longer required, all erosion protection, hay bales, silt fence barriers, etc., as indicated on the Contract Drawings and as required.
   D. Include protection of all new and existing storm sewer inlets, structures, manholes, catch basins, etc. from soil infiltration using posts, hog wire fencing, filter fabric and hay bales. Maintain protection throughout the duration of the project and until final acceptance.
   E. Maintain positive drainage away from new construction areas for the duration of project. NOTE: It will be CRITICAL to establish a temporary means of addressing storm water that currently runs through the project site towards the southwest corner. Include installation and maintenance of Temporary Sediment Basin.
   F. Replace existing sod, landscaping, etc. where your work encroaches on areas outside the primary construction site or where new sod, landscaping, etc. are not indicated on the landscaping plan.
   G. Maintain all items installed under this section throughout the duration of the project or until no longer required.

3. Demolition, clearing and grubbing includes:

A. All demolition as required by the Contract Documents.
B. All clearing and grubbing as required by the Contract Documents.
C. Remove all debris from the site and properly dispose of off-site. No burning will be allowed on site.
D. Stripping of all topsoil as indicated or required by the Contract Documents.
   1. Stockpile topsoil on-site in location approved by the Construction Manager.
   2. Protect stockpiled topsoil from erosion. Maintain erosion control measures until no longer needed.
   3. Periodically turn over topsoil to promote composting. At a minimum, perform this work as necessary to prevent the growth of weeds or other unwanted growth within the stockpiled topsoil.
   4. Redistribute, spread and fine grade topsoil as required by the Contract Documents.
      a. Topsoil distribution, spreading and fine grading will be performed during the later stages of the project.
   5. Provide additional topsoil as required to comply with the requirements of the Contract Documents. Distribute, spread and fine grade all topsoil provided.
      a. Topsoil distribution, spreading and fine grading will be performed during the later stages of the project.
E. Removal of all trees (including stump and root removal) within the limits of construction and not specifically noted to remain.
F. Remove and reinstall existing fencing as necessary to perform your work.
G. Include all sawcutting as necessary or required in the performance of your work.
H. Coordinate all required mechanical and electrical equipment removal with the respective trades.

4. Relocation and removal of existing site utilities includes:
   A. Relocate existing site water, fire, irrigation, storm and sanitary sewer lines as required by the Contract Documents.
      1. Existing utilities must remain in service until ready for final tie-in of new utility.
   B. Schedule all required utility interruptions with the Construction Manager no less than one (1) week prior to the utility interruption.
   C. Notify the Construction Manager immediately and in writing of any unidentified utilities encountered during the course of your work.

5. Excavation, Backfill and Grading includes:
   A. All earthwork, excavation, cut, fill, backfill and compaction required to perform your work in accordance with the Contract Documents.
   B. Include all import material required by the Contract Documents.
   C. Include proof-rolling as required to meet all required soil densities.
   D. Include all water necessary for obtaining optimal compaction.
   E. All compaction shall be in lifts as specified.
   F. Include all fill required to backfill areas adjacent to buildings, behind retaining walls, inside planting beds, behind sidewalks, behind curbs, etc.
      1. Immediately prior to the start of landscaping work, fine grade all unpaved areas, landscaped areas, planting bed areas, etc. to plus or minus 0.1 feet. Coordinate final grading operations with the Landscaping Subcontractor to ensure that areas to receive landscaping are provided at the required grade.
   G. Include sufficient fill as required to compensate for any materials that are removed during the demolition of existing site construction and utilities.
   H. Construct all building pads.
      1. Building pads shall be stabilized to 10' outside the building corners. Coordinate with any tree save areas and tree protection.
      2. Provide and grade building pads and surrounding work to plus or minus 0.1 feet.

I. At or near project completion, fine grade the project site to plus or minus 0.05 feet.
J. Distribute excess fill from other trades' excavations as required. Excess fill within the building pad will be removed by the responsible subcontractor and distributed or removed from site by this Subcontractor (Site Work Subcontractor).
K. Include all de-mucking and/or dewatering required to perform your work.
L. All unsuitable materials excavated in the course of your work shall be disposed of off-site and replaced with approved fill.
   1. No additional compensation will be provided for unsuitable materials encountered or for replacement fill providing it is within the general scope of the soils report.
   2. Replacement of unsuitable soils outside the scope of the soils report shall be performed at the unit prices provided on the Bid Proposal Form.
   3. No payment will be made for the replacement of unsuitable material unless authorized in writing by the Construction Manager prior to the performance of the work.
   4. Maintain proper documentation of quantities for all items that are compensated on a unit price basis. Proper documentation shall include the Construction Manager's daily verification of work performed by this Subcontractor.
M. All fill materials utilized by this Subcontractor for foundation fill, building pad fill, and any other work located within the footprint of the building(s) shall have radium concentration levels which comply with the recommendations and guidelines set forth by the United States Environmental Protection Agency. This shall apply to both imported fill and fill obtained from on-site cut/fill operations. This Subcontractor shall perform and pay for all testing and certifications necessary in substantiating compliance with this requirement. The Construction Manager shall be provided copies of all test results and certifications. Refer to the Contract Documents for requirements related to testing/replacing undisturbed soil within the building(s) footprint(s).

6. Site Water System(s) include:
   A. All on-site and off-site water systems from five feet (5') outside the point of building entry to existing or proposed utilities in accordance with Contract Documents.
   B. Make all connections to existing or proposed utilities. Coordinate connections with local agencies.
   C. Furnish and install all related fittings, valves (gate, shutoff, butterfly, balancing, pressure reducing, etc.), meters, backflow preventors, check valves, double detector check valve assemblies, and all other appurtenances required by the Contract Documents or required by code. Include all required sleeves, thrust blocks, concrete pads, insulated cover assemblies, etc. (i.e. all items required for a complete and fully operational installation).
   D. Connections at five feet (5') outside the point of building entry will be by others. This Subcontractor is responsible for providing the location and elevation for all terminations and/or points of connection by others.
   E. Disinfect system at completion of your work and just prior to connection of building system. All bacteriological tests shall be performed and approved by all state and local agencies.
   F. Provide all meters, vaults, hatches and associated hookups.
   G. Include all connection(s) to water main source(s).
   H. Certify all installations as required by state and local agencies.

7. Site Fire System(s) include:
   A. All on-site and off-site fire water systems from one foot (1') above finished floor inside the building to existing or proposed utilities in accordance with Contract Documents.
      1. Include blind flange at one foot (1') above finished floor inside the building for connection by others.
   B. Include all fire hydrants, Siamese connections, fire department connections and related piping.

C. Make all connections to existing or proposed utilities. Coordinate connections with local agencies.
D. Furnish and install all related fittings, valves (gate, shutoff, butterfly, balancing, pressure reducing, etc.), meters, backflow preventors, check valves, double detector check valve assemblies, and all other appurtenances required by the Contract Documents or required by code. . Include all required sleeves, thrust blocks, concrete pads, insulated cover assemblies, etc. (i.e. all items required for a complete and fully operational installation).
E. Connections at one foot (1') above finished floor inside the building will be performed by others. This Subcontractor is responsible for providing the location and elevation for all terminations and/or points of connection by others.
F. Disinfect system at completion of your work and just prior to connection of building system. All bacteriological tests shall be made and approved by all state and local agencies.
G. Provide all meters, vaults, hatches, and associated hookups.
H. Include connection(s) to water main source(s).
I. Certify installations as required by local and state agencies.

8. Site Sanitary Sewer Systems include:
   A. All on-site and off-site sanitary sewer systems from five feet (5') outside the point of building entry to existing or proposed utilities in accordance with Contract Documents.
   B. Make connections to existing or proposed utilities. Coordinate installation with local agencies.
   C. Connections at five feet (5') outside the point of building entry will be by others. This Subcontractor is responsible for providing the location and elevation for all terminations and/or points of connection by others.
   D. Include all costs to provide TV inspections, if required by the Contract Documents.
   E. Include all pre-cast manholes and covers.
   F. Include all cleanouts and covers.

9. Site Storm Water System includes:
   A. All on-site and off-site storm water drainage systems outside the point of building entry or point of connection for building systems to point of discharge or connection to existing system in accordance with the Contract Documents.
      1. Include all rainwater, downspout and roof drain collection systems.
   B. All catch basins, outfall structures, skimmers, culverts, grates, mitered ends, manholes, control weirs and splash blocks. Structures shall be installed in alignment with adjacent buildings, roadways, etc. to provide an architecturally acceptable appearance.
   C. Include protection of entire system, including holding ponds and/or basins, for the duration of the project.
   D. Coordinate roof drain and downspout tie-in locations with the appropriate contractors. Provide storm sewer service to all points of connection. Accommodate tie-ins (by others) to your system via tees, saddles, sleeves, structure cut-outs, etc. (it is the intent that your system not require modifications by others in order to perform their tie-ins). This Subcontractor is responsible for providing the location and elevation for all terminations and/or points of connection by others.
   E. Include costs to test all lines per the Contract Documents.
   F. Flush entire system clean prior to the substantial completion inspection for the project and, if necessary, perform remedial flushing and cleaning prior to the final completion inspection for the project.
   G. Include all site area drains.
   H. Include all trench drains and related covers/grates.
   I. Include all subdrainage systems, including planter drains, underdrains, foundation drains, french drains, etc. as required by the Contract Documents. Include all porous fill, geofabric, drain tiles, etc. for a complete installation. The scope of this work is not limited to items shown on the Civil Drawings. Carefully review all Civil, Landscaping, Structural and Architectural drawings, wall sections and details

to determine the extent of this work. All subdrainage systems shall be installed in accordance with the Contract Documents. Coordinate your installations with other trades as necessary.

10. Modular Concrete Retaining Wall Systems
    A. Include all modular concrete retaining walls as shown on the Contract Documents.
        1. Include all sleeves under or through the retaining walls.
        2. Refer to Sheets C300 and S1.05 for details on the retaining wall.
    B. Perform all layout and field engineering required in the performance of your work.
    C. Include all pads, pins, geogrid, and accessories required in the performance of your work.
    D. Furnish and install all waterproofing membranes, waterproofing systems, and other required membranes that are to be applied under your work.
    E. Furnish and install all fill soils for the proper installation of your work.
    F. Furnish and install all expansion joint, control joint, and isolation joint assemblies as indicated and/or required.
    G. Include all piping, drains and weeps.
    H. Prior to completion, point, patch and fix any chips, nicks, scratches, or minor abrasions caused during construction.
    I. Protect all walls once completed.

11. Asphalt and Concrete Paving includes:
    A. All concrete paving (at roadways and/or intended for vehicular traffic), asphalt paving, asphalt resurfacing, base, sub-base, curbs, curb and gutter, sidewalks, sub-grade preparation, striping, pavements markings, wheel stops, and signs as required by the Contract Documents.
    B. Protect and cure all paving as specified prior to striping and/or allowing traffic on paving.
    C. All tie-ins with existing paving shall be performed in a neat, workmanship-like manner. Saw-cut existing paving as necessary to obtain smooth edges in which to tie into.
    D. Include all striping, pavement markings, signs and wheel stops in accordance with the Contract Documents.
    E. Include all detectable warnings in your work as indicated on the Contract Documents.

12. Removal and replacement of existing improvements includes:
    A. The removal and replacement of existing improvements (i.e. curbs, base, paving, sidewalks, landscaping, sodding, planting beds, etc.) necessary in the performance of your work and where new construction is not indicated in the Contract Documents.
        1. Perform for all off-site work.
        2. Perform for on-site work where new construction (that would replace items removed) is not indicated.
    B. The condition of existing improvements shall be thoroughly documented by this Subcontractor prior to the start of any work.
    C. Replacement construction for existing improvements removed and/or affected in the course of your work shall meet or exceed the level of quality, materials, workmanship, etc. in their pre-construction condition.
    D. Replacement construction for existing improvements removed and/or affected in the course of your work shall be performed as soon as practical.

13. General items applicable to all of the above as appropriate:
    A. Coordinate all off-site utility work, utility shutdowns, street closings and all cutting and patching of existing streets with the Construction Manager. Provide a minimum of 72 hours notice.
    B. Locate and protect all existing utilities that are to remain in service.
    C. This subcontractor is responsible for capping, staking and providing GPS coordinates and elevations for

all terminations for connection by others, either as a part of this Project or by the Owner in the future. This Subcontractor shall assist in locating any and all connection points not properly located or otherwise lost.

D. All capped and staked lines shall be located exactly on as-built drawings. Stake lines with 4"x 4" post.
E. This Subcontractor shall include all tie-ins to existing utilities, street cuts & patching, taps, fees, permits, and jacking and boring required to perform your work.
F. Include all concrete, formwork, and reinforcing related to this scope of work.
G. All systems shall be tested in strict accordance with the Contract Documents prior to backfilling.
    1. Subcontractor must comply with all notice requirements in the Contract Documents prior to performing any tests.
    2. A test log will be provided in the office of the Construction Manager. Log shall be kept current at all times.
    3. All tests must be witnessed and signed off by the Construction Manager at a minimum, and others as required by the Contract Documents and applicable codes.
H. This subcontractor shall schedule all applicable tests and/or inspections with local agencies.
I. Schedule all shutdowns with the Construction Manager so as to provide minimal impact to existing facilities. No systems shall be cut off or taken out of service without specific written authorization from the Construction Manager.
J. All tests must be scheduled in writing at least 48 hours in advance through the Construction Manager. All costs for re-testing non-conforming work shall be borne by this subcontractor.
K. Include all layout and engineering required to perform your work and to maintain site control points.
L. This Subcontractor will be responsible for maintaining current as-built documents at all times, including the Construction Manager's master as-built documents and the Subcontractor's working as-built documents. The as-built drawings will be reviewed monthly by the Construction Manager's Superintendent and must be up to date as a condition precedent to the release of monthly draw. At or near project completion, this Subcontractor shall submit to the Construction Manager, a final set of as-built documents which shall be certified by a Georgia Licensed Surveyor if required by the Contract Documents or governing agencies.
M. Include clean-up of your work on a daily basis. Remove all debris from the site and dispose of off-site in a lawful manner. Also reference scope item B.2-14.
N. Provide all hoisting and material handling required to perform your work.
O. Coordinate and perform all work in compliance with all federal, state, county and city agencies having jurisdiction.
P. Properly barricade all construction areas.
Q. Include necessary warning signs.
R. Provide flagmen as necessary at public areas.
S. Provide all required concrete thrust blocks.
T. Install all pipe bollards located in your work. Pipe bollards will be furnished by others. Include concrete foundations and fill for bollards.
U. Include painting of all exposed piping, hydrants and miscellaneous metals in accordance with the specifications.
V. Include protection for and identification of all underground piping.
W. Include all necessary embeds, brackets, supports, fasteners, etc., required to perform your work.
X. Provide miscellaneous small tools and specialized tools as noted and required by the Contract Documents.
Y. Copies of the subsurface exploration soils reports are part of this Bid Package.
Z. Notify Construction Manager in writing of any unidentified utilities, obstructions or unforeseen conditions encountered.

AA. Quantities on drawings are for clarification and are approximate. This subcontractor is required to provide all piping, accessories and other material/items necessary to provide a complete installation.
BB. Include all required sheeting and shoring. Provide trench box for all excavations over 5 feet deep.
CC. Include all dewatering required in the performance of your work.
DD. Include cleaning (sweeping) of adjacent roadways and parking areas at least once per week throughout the construction duration to remove unwanted sediments. Provide one final sweeping at project material completion and another at project final completion.
EE. Identify and protect all structures, back flows, and stub-ups with a minimum of 2 x 4 pins around all sides.
FF. Camera all new underground sanitary sewer utility lines per the Contract Documents and transmit video to Construction Manager before final acceptance.
GG. Include all GDOT barricades and flagmen as required to perform your work.
HH. Include all brick coursing, fillets, rip-rap, polyethylene sheeting, gravel, etc. required for complete installations.
II. Multiple mobilizations will be required to complete the work included in this Bid Package.

14. Cleanup
    A. This Subcontractor shall provide <u>daily</u> clean-up of all debris resulting from the work of the Bid Package. Clean-up shall take place continuously throughout each day. Should the Subcontractor fail to clean-up the previous day, <u>prior</u> to the start of <u>any</u> work the next day, this Subcontractor shall clean-up all debris. Upon eight hour notice, the Construction Manager may perform the Subcontractor's clean-up and deduct all costs from the Subcontract Agreement.
    B. In addition to the above requirement, this Subcontractor will be required to provide labor manpower for general project clean-up as listed below. This manpower will be under the direction of the Construction Manager. As a part of this Subcontractor's base bid for the project, this Subcontractor shall provide <u>1</u> worker for 8 hours each, <u>1</u> day per week, for a total duration of <u>30</u> weeks for general project clean-up.
    C. Dumpsters will be provided by the Construction Manager for construction debris only, not Sitework waste or soil spoils. The dumpster location(s) will be designated by the Construction Manager. It is the responsibility of the Subcontractor to remove construction debris from the building or site and to place the construction debris into the dumpsters.
        1. The following additional materials will not be allowed in dumpsters and it is this Subcontractor's responsibility to dispose of these items in a lawful manner: hazardous materials of any kind, buckets of any size, carpet remnants, household trash, perishable items, liquids, appliances, and computers.

B.3 ADDITIONAL PROJECT SPECIFIC REQUIREMENTS

1. This Subcontractor shall include in his base bid an allowance of 300 cubic yards of recycled concrete, gravel and other suitable base/subgrade material installed for use as temporary entrances and drives. Installation shall be as directed by the Construction Manager. Allowance shall include furnishing, installing, compacting, maintaining, removing and disposing of this material. Include unit price for adjustments to this allowance on the Bid Proposal Form. Do not exceed allowance quantity without written approval from the Construction Manager. Upon completion of the work, a change order will be issued to the Site Work Subcontractor to reconcile the difference between this allowance and the actual quantities provided for the project.

2. BIM (Building Information Modeling) software shall be utilized as part of the Design, Shop Drawing Submittal, Review and Coordination, as well as the Final As-Builts for the following trades: Structural,

Mechanical, Electrical, Plumbing, and Fire Protection. All costs to provide these services will be borne by the respective subcontractors.

3. LEED: All subcontractors are required to assemble, document, and submit necessary information to the CM in order to provide timely information to the A/E regarding LEED materials and recordkeeping.

4. Escrow Documents shall be submitted per 0700-108 of contract between CM and Fulton County shall be submitted within 10 days after the bid date if requested by the CM.

5. First Source Jobs Program will be utilized for entry-level hires.

6. Per the Contract Documents, prior to Substantial Completion confirm City of Roswell and Atlanta-Fulton County Public Library requirements. Submit copies of any required maintenance bonds, professional testing or reports, and inspections. Coordinate submittal with the Construction Manager.

7. All tap fees and related coordination costs with Fulton County shall be borne by the applicable subcontractor. All trade specific permitting cost shall be <u>included</u> in your bid proposal.

8. All Subcontractors are required to give 72 hours of advance notice of any testing activities to the CM to allow for proper notification of the Owner's Representative.

9. Inclement Weather Days shall be per section 00700-53 of contract between CM and Fulton County, which lists the normal Monthly breakdown of inclement weather days. No time extensions or cost adjustments will be allowed for normal inclement weather.

10. Include temporary construction fencing, safety fencing and barricades required for all off-site work.

11. This subcontractor shall provide all tree protection noted on LS1.0 prior to commencement of Site activities and maintain it in acceptable condition throughout the course of construction. Coordinate tree protection with Surcharge Plan.

12. Coordinate with the Construction Manager and Owner per the note on LS1.0 to establish a stockpile in which local volunteers can harvest/gather the resurrection ferns and branches of the 60" and 42" historically significant trees that are scheduled for removal.

13. Coordinate with the Construction Manager and provide a 24" section of each of the historically significant trees that will be used for an Architectural feature inside the building.

14. Reference the Subsurface Exploration and Geotechnical Engineering Evaluation for the East Roswell Branch Library from Willmer Engineering, Inc. dated August 03, 2012. Include all costs related to the identification and undercutting of existing fill soils, installation of acceptable fill soil material following all placement procedures and compaction requirements.

15. This subcontractor shall proof-roll all areas in accordance with the Contract Documents.

16. Borrow Source approval is required per the Geotechnical Report item 5.4.1. Within 10 days of mobilization this subcontractor shall submit all required information to the Construction Manager.

17. Provide maintenance of all sediment and erosion controls throughout construction and removal as mandated

by progress and/or phasing. No additional costs will be accepted for these activities. This includes all Construction Exits, Temporary Mulching, Temporary Grassing, Permanent Grassing, Dust Control, Silt Fencing, Inlet Protection and Sediment Traps, Outlet Protection, Wash-down Areas and Erosion Control Matting and Blankets. Maintenance shall include all re-grading, watering, and mowing of vegetative measures.

18. Provide any sampling and reporting per the requirements of NPDES, EPD, and City of Roswell. This subcontractor shall supply all required documentation and coordination efforts to the Construction Manager in a timely manner for submittal.

19. Coordinate installation of Water Quality Devices (Water Quality Control Structures and Infiltration Trenches) with the Construction Manager per the Contract Documents. Any cost associated with rework or remedial work due to lack of coordination will be the responsibility of this subcontractor.

20. At or near completion install 6" of crusher run stone and 12" steel edging at overhang per Sheet A1.00.

21. All sidewalks, driveways, curbs, hardscape and concrete paving shown on C300 will be performed as part of this Bid Package.

22. Coordinate with the Owner's CxA and provide all necessary manpower, equipment, and testing during the commissioning process.

23. This subcontractor acknowledges that equipment for portions of the work will be started, tested, run and otherwise utilized prior to start of the warranty period. This subcontractor will include all costs required to insure that all warranty periods commence at the date of Final Completion.

24. No additional cost(s) or Change Orders for expediting material in order to meet the known Construction Schedule will be considered.

25. All manufacturer lead times and/or fabrication times for any components of your work that could be defined as "long-lead" items shall be included with your bid. Be advised that lead times are to be figured from issuance of Purchase Order or ODP.

26. Include all removal of existing bike paths and replacement as indicated on the Construction Documents.

27. Furnish, install and maintain all temporary sediment basins as indicated on the Construction Documents.Reference P1.0 for Site Fire that runs underneath the building pad. This portion of the work is to be installed by the Sitework subcontractor per B2, item 7. Instead of stubbing up into the basement, the fire piping will stub down into the basement. Coordinate elevation and location of this piping with the CM.

B.4 WORK EXCLUDED FROM THIS BID PACKAGE

1. Soil and concrete materials testing will be performed by the Owner with the following exceptions.
   A. Subcontractor shall perform and pay for all testing and certifications related to compliance with the US EPA's recommendations and guidelines regarding radium concentration levels in imported fill and on-site borrow fill utilized for foundation fill, building pad fill, and any other work located within the footprint of the building(s).
2. Exclude unit pavers. This work will be performed by others.
3. Exclude temporary construction fencing for the main construction site. This fencing will be installed by

others.

4. All Waterproofing associated with foundation walls at the building is by others.

B.5 BID ALTERNATES AND VOLUNTARY ALTERNATES

BID ALTERNATES

This Subcontractor shall provide pricing for the following Bid Alternates on the Proposal Form. The Bid Alternates provided on the Proposal Form shall be used for the purpose of adjusting this Subcontractor's Base Bid if such Alternate(s) is(are) accepted.

1. **Surcharging of the Building Pad-** At the present time the Civil Engineer is finalizing a surcharge plan for the East Roswell Library. However, we felt it was important to advise all Sitework subcontractors and evaluate initial costs separate from the Base Bid. To that end, the Construction Manager has drafted a basic scope of the anticipated activities to price as a Bid Alternate.

   After the building pad has been brought to proposed subgrade this subcontractor shall commence the surcharge phase of the project as delineated in the Geotechnical Engineering Evaluation for East Roswell Branch Library. For the purposes of the bid alternate, assume the following:

   It has been estimated that approximately 5000 CY of fill will be required to complete the required surcharging of the building pad. If the surcharge fill is determined to be acceptable (by testing), it may be utilized at parking and other areas onsite after the two-month surcharge at the building is complete, or it can be removed from site and disposed of by this subcontractor at the end of the surcharge period. This Subcontractor shall furnish, install and maintain all additional erosion control methods for the Surcharge Phase including, but not limited to mulching of the surcharge and installation of temporary drains and sediment storage areas. Provide and maintain temporary access to and from the pad to allow for efficient and safe movement of materials. All permanent retaining walls, site walls, and foundation walls will commence <u>after</u> the Surcharge Phase is complete. As such, this subcontractor will provide all secondary excavation required for the safe installation of these structures. Methods utilized will be reviewed by the Construction Manager and Civil Engineer and can include temporary earth retention systems, benching and sloping, etc. At the completion of these activities this Subcontractor will install any foundation drain systems, backfill and re-compact these locations as necessary to finalize the building pad.

2. **Delete Entrance Canopy drainage system.** In lieu of the Aluminum Entrance canopy shown, only a 10'x10' entrance canopy over the doors would be installed. Canopies over the service entrance and drive up book return will remain in the base bid. Architect's Alternate No. 04.

VOLUNTARY ALTERNATES

This Subcontractor will have the opportunity to provide Voluntary Alternates on the Proposal Form. This Subcontractor shall utilize the Voluntary Alternate section of the Proposal Form, and only this section, to offer bid adjustments for value engineering options, discounts for the award of multiple bid packages, alternative materials, alternative equipment, alternative methods, etc. All Voluntary Alternates offered on the Proposal Form must include a detailed description of the proposed alternate, including the effects that the alternate will have on other trades (provide additional details as an attachment to the Proposal Form if

necessary). The Voluntary Alternates provided on the Proposal Form shall be used for the purpose of adjusting this Subcontractor's Base Bid if such Alternate(s) is(are) accepted.

B.6 UNIT PRICES

The following is a list of unit costs to add/deduct labor, material and equipment, including all labor burden, taxes, overhead, bonds, incidental tools, profit, etc., as required to provide a complete unit cost.

Add/Deduct in Temporary Drive Allowance	$_____/Cubic Yard
Removal and Replacement of Unsuitable Soils	$_____/Cubic Yard
Add/Deduct Type C Erosion Control Fencing	$_____/Linear Foot
Add/Deduct Street Sweeping	$_____/Each Sweeping
Add, Maintain & Remove Truck Washdown	$_____/Washdown System
Add/Deduct Concrete Washdown	$_____/ Washdown

END OF SCHEDULE "A"

ATTACHMENT C

INSURANCE COVERAGE REQUIREMENTS

WORKER'S COMPENSATION

State:	Statutory requirements
Applicable Federal: (For example, Longshoremen's)	Statutory requirements

COMPREHENSIVE GENERAL LIABILITY	Minimum Limits
Bodily Injury:	$1,000,000.00 Each Occurrence
Property Damage:	$1,000,000.00 Each Occurrence

Including Premises-Operations; Independent Contractor's Protective; Products and Completed Operations, Personal Injury and Advertising Injury assumed under an insured contract, including Tort Liability of another assumed in a contract; Broad Form Property Damage; Explosion, Collapse and Underground Coverages; and Products coverages.

If the Commercial General Liability Policy ("CGL") contains a general aggregate limit, it shall apply separately to this Subcontract. The CGL insurance shall be written on ISO occurrence form CG 00 01.

Contractor, Owner and Architect must be spelled out on certificate and shall be included as additional insureds under Subcontractor′s CGL policy and, if necessary, umbrella liability insurance using ISO additional insured endorsement CG 20 10 07/04 edition and shall include a completed operations additional insured endorsement CG 20 37 07/04 edition.

This insurance shall apply as primary insurance with respect to any other insurance or self-insurance afforded to Contractor. There shall be no endorsement or modification of the CGL to make it excess over other available insurance.

Subcontractor shall maintain CGL and, if necessary, commercial umbrella liability insurance with a limit not less than $1,000,000 each occurrence for at least three years following final payment for the Work. The policy shall provide a Products and Completed Operations aggregate of at least two times its each occurrence limit. Continuing CGL insurance shall be written on ISO occurrence form CG 00 01 (or a substitute form providing equivalent coverage) and shall at minimum cover liability arising from Products and Completed Operations and liability assumed under an insured contract.

COMPREHENSIVE AUTOMOBILE LIABILITY	Minimum Limits
Bodily Injury:	$1,000,000.00 Each Occurrence
Property Damage:	$1,000,000.00 Each Occurrence

Comprehensive Automobile Liability shall include coverage for any owned autos, non-owned autos and hired autos.

CERTIFICATE FORM REQUIREMENTS

All certificates must be issued on an ACORD form.

In addition to the additional Insureds being spelled out in the description section of the certificate, the project name, number, and address must also be included.

The certificate shall be executed with a "live" signature by a duly authorized representative of each insurer and shall provide for a 30 day written notice prior to cancellation.

PROPOSAL FORM

PROPOSAL FOR: EAST ROSWELL LIBRARY
2301 HOLCOMB BRIDGE ROAD
AJAX PROJECT NO. 201209

BID PACKAGE NO: 2.1

ENTITLED: SITEWORK & UTILITIES

PROPOSAL OF: _____
(Bidder)

DATED: _____

TO: AJAX BUILDING CORPORATION
c/o FULTON COUNTY DEPARTMENT OF PURCHASING AND CONTRACT COMPLIANCE
130 PEACHTREE STREET S.W., SUITE 1168
ATLANTA, GA 30303

1. The Bid Package referenced herein is entitled "Bid Package" No. _____

2. _____, the undersigned, do hereby declare that we have carefully examined the site of the proposed Work and the contract documents. We do hereby agree to furnish all material, transportation, equipment, apparatus systems, labor and supervision required to do all Work in strict accordance with the Contract Documents for the following Base Bid price:

A. BASE BID (Single Bid)

Bid Package No. _____

Total bid price for all Work, complete, in accordance with the Contract Documents inclusive of the above referenced Bid Package:

_____ Dollars ($_____)
(excluding P & P Bonds)

* All lines not used in proposal must be filled in as Not Applicable.

B. BID ALTERNATES (Refer to Bid Package, Schedule "A", Section B.5.)

The following Alternate Pricing is provided for the purpose of adjusting the Bidder's Base Bid if such Alternate(s) is(are) accepted. Refer to Bid Package, Schedule "A", Section B.5. for specific requirements and a detailed description of alternates. Note: If your proposal reflects more than one bid package identify which bid package the proposed alternate is for.

1) DESCRIPTION OF ALTERNATE:
Surcharging of the Building Pad, as described in Scope of Work item B.5-1.

Add / Deduct / No Change Dollars $ _____

(excluding P & P Bonds)

2) DESCRIPTION OF ALTERNATE:
Delete Entrance Canopy drainage system. Architect's Alternate No. 04.

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

3) DESCRIPTION OF ALTERNATE:

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

4) DESCRIPTION OF ALTERNATE:

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

5) DESCRIPTION OF ALTERNATE:

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

C. VOLUNTARY ALTERNATES

The following Alternate Pricing is provided for the purpose of adjusting the Bidder's Base Bid if such Alternate(s) is(are) accepted. Bidder shall provide a detailed description of each proposed alternate, including the effects that the alternate will have on other trades (provide additional details as an attachment if necessary). Note: If your proposal reflects more than one bid package identify which bid package the proposed alternate is for.

1) DESCRIPTION OF ALTERNATE:

_____

_____

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

2) DESCRIPTION OF ALTERNATE:

_____

_____

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

3) DESCRIPTION OF ALTERNATE:

_____

_____

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

4) DESCRIPTION OF ALTERNATE:

_____

_____

_____

_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

5) DESCRIPTION OF ALTERNATE:

_____
_____
_____
_____

Add / Deduct / No Change Dollars $ _____
(excluding P & P Bonds)

D. UNIT PRICES (Refer to Bid Package, Schedule "A", Section B.6.)

IMPORTANT NOTE: Work outlined in Schedule "A" of the Subcontract Agreement shall be bid and awarded as a lump sum Contract. The unit prices on this proposal form may be used as a basis for payment for any changes in scope. Unit prices are inclusive of all costs except Payment and Performance Bond. Payment and Performance Bond shall be added/deducted in accordance with Item 3.B. of this Proposal. No additional overhead, profit, tax, insurance, etc. will be allowed. Note: If your proposal reflects more than one bid package identify which bid package the proposed unit prices are for.

DESCRIPTION OF UNIT

1) Add/Deduct in Temporary Drive Allowance Dollars $ _____/Cubic Yard

2) Removal and Replacement of Unsuitable Soils Dollars $ _____/Cubic Yard

3) Add/Deduct Type C Erosion Control Fencing Dollars $ _____/Linear Foot

4) Add/Deduct Street Sweeping Dollars $ _____/Each Sweeping

5) Add, Maintain & Remove Truck Washdown Dollars $ _____/Washdown

6) Add/Deduct Concrete Washdown Dollars $ _____/Washdown

7) _____ Dollars $ _____

8) _____ Dollars $ _____

9) _____ Dollars $ _____

10) _____ Dollars $ _____

E. Detailed Back-up will be required for change orders. This will include direct labor costs. These labor costs will be subject to a multiple to cover Burden/Fringes (Workman's com, vacation, holidays, etc.). Enter the burden rate percentage for your company _____%. Documentation may be required for verification.

3. PAYMENT AND PERFORMANCE BONDS

The cost of Payment and Performance Bond premiums shall not be included in the Proposal Sum (Base Bid, Alternates or Unit Prices). The cost to add/deduct Payment and Performance Bond premiums to the Proposal Sum are as follows (Note: Documentation may be required for verification of bond costs):

A. Add Payment and Performance Bonds to Base Bid. Dollars $_____

B. Add/Deduct Payment and Performance Bonds to Alternates, Unit Prices and/or Change Orders. Percent _____%

4. Bid Security in the sum of 5% of Proposal Sum _____Dollars ($ _____) in the form of _____ is submitted herewith.

5. This proposal complies with the Notice to Bidders dated _____(including all Contract Documents referenced therein, and all Addenda, hereinafter listed and acknowledged as received), which are hereby made a part hereof and which shall govern in all matters of the Work hereby proposed. We acknowledge receipt of the following Addenda:

(Bidder to list all revisions received, or, if none, state "NONE RECEIVED".)

Addendum # _____ dated _____ Addendum #_____ dated _____

Addendum # _____ dated _____ Addendum #_____ dated _____

Addendum # _____ dated _____ Addendum #_____ dated _____

Addendum # _____ dated _____ Addendum #_____ dated _____

6. What percentage of the work do you propose to utilize MBE contractors for: _____%.

7. The bidder acknowledges that all excavation work must comply with the OSHA Trench standards 29 CFR 1926, 650, 651, and 652 and has included the cost of this compliance in their proposal in the form of:

	Method of Protection	Estimated Quantity/Unit	Cost Per Unit	Total
1.	_____	_____	_____	_____
2.	_____	_____	_____	_____
3.	_____	_____	_____	_____
4.	_____	_____	_____	_____

BIDDER: _____

ADDRESS: _____

_____

TELEPHONE NUMBER: _____

By: (Member of Firm Authorized to Sign Bid): _____

Title: _____

Seal Required for Corporation

State Certificate Number: _____

The Bidder is a/an:
( ) Individual
( ) Partnership
( ) Corporation, incorporated in the State of _____

BID PROPOSAL AFFIDAVIT

(The following Affidavit shall be executed)

STATE OF)
COUNTY OF) ss.

_____, of lawful age, being first duly sworn, upon his oath deposes and says: That he executed the accompanying Proposal on behalf of the subcontractor therein named, and that he had lawful authority to do so, and said subcontractor has not directly, or indirectly entered into any agreement, expressed or implied, with any other subcontractor(s) or person(s), having for its object the controlling of the price or amount of such Proposal, or any other proposal, the limiting of the number of Proposals or subcontractors, the parceling, or farming out of any profits thereof to any subcontractor(s), or other person(s), and further says that he has not and will not divulge the sealed Proposal to any other person, except those having a partnership or other financial interest with him in said Proposal or Proposals, until after the sealed Proposal or Proposals are opened.

Signed: _____

Sworn to and subscribed before me this

_____ day _____, 20__

_____
(Notary Signature)

Notary Public, State of _____

My Commission Expires:

CONSTRUCTION SCHEDULE

CONSTRUCTION TIME

The construction documents describe the Scope of Work for the completion of the contract. The duration and start date of each activity will be as per the duration and early start date as shown on Ajax Building Corporation of Georgia's Project Schedule.

The following schedule reports are attached:

1. Responsibility Sort — Sorted by early start listing all activities that will be the responsibility of the Subcontractor performing the work of this Bid Package.

East Roswell Library
Bid Package Schedule

ID	Task Name	Duration	Early Start	Early Finish	Predeces	Successor	Text1
54	**Completion of Documents & Permitting**	**55 days**	**Fri 3/1/13**	**Thu 5/16/13**			
56	**Permitting**	**55 days**	**Fri 3/1/13**	**Thu 5/16/13**			
57	**Land Disturbance Permit**	**43 days**	**Fri 3/1/13**	**Tue 4/30/13**			
63	Issue LDP Permit	0 days	Tue 4/30/13	Tue 4/30/13	62		Mile
70	**NPDES Permit**	**26 days**	**Wed 4/3/13**	**Wed 5/8/13**			
73	Issue NPDES Permit	0 days	Wed 5/8/13	Wed 5/8/13	72		Mile
64	**Building Permit**	**55 days**	**Fri 3/1/13**	**Thu 5/16/13**			
69	Issue Bldg Permit	0 days	Thu 5/16/13	Thu 5/16/13	68	374	Mile
74	**Procurement Phase**	**106 days**	**Thu 5/16/13**	**Thu 10/10/13**	**51**		
75	**Bid Group A**	**76 days**	**Thu 5/16/13**	**Thu 8/29/13**			
79	**BP 2.1 Sitework**	**43 days**	**Thu 5/16/13**	**Mon 7/15/13**			
81	Execute Subcontract	2 days	Fri 5/17/13	Mon 5/20/13	80	82,306,3(	2.1
82	Prepare Submittals	5 days	Tue 5/21/13	Mon 5/27/13	81	83	2.1
85	Fab & Deliver Basic Materials	5 days	Tue 6/18/13	Mon 6/24/13	84	319	2.1
88	Fab & Deliver Water/Fire Main Mtrls	10 days	Tue 6/18/13	Mon 7/1/13	84	329,386	2.1
86	Fab & Deliver Storm Str/Pipe	20 days	Tue 6/18/13	Mon 7/15/13	84	319	2.1
87	Fab & Deliver SS Str/Pipe	20 days	Tue 6/18/13	Mon 7/15/13	84	325	2.1
300	**Construction Phase**	**308 days**	**Fri 5/31/13**	**Wed 8/6/14**			
301	**Site Construction**	**281 days**	**Fri 5/31/13**	**Mon 6/30/14**			
324	**Sanitary Sewer System**	**7 days**	**Thu 8/15/13**	**Fri 8/23/13**			
325	Make SS Tap	1 day	Thu 8/15/13	Thu 8/15/13	87,319	326	2.1
326	Install SS Piping and Structures	5 days	Fri 8/16/13	Thu 8/22/13	325	327,329,:	2.1
327	Put SS in Service	1 day	Fri 8/23/13	Fri 8/23/13	326	776	2.1
302	**Bldg Pad**	**73 days**	**Fri 5/31/13**	**Wed 9/11/13**			
303	Construction Start	0 days	Fri 5/31/13	Fri 5/31/13	53	305	Mile
306	Clear & Grub	5 days	Thu 6/6/13	Wed 6/12/13	304,81	308	2.1
307	Establish Erosion Control Measures	5 days	Thu 6/6/13	Wed 6/12/13	304,81	309	2.1
308	Fill & Proofroll Bldg Pad	10 days	Thu 6/13/13	Wed 6/26/13	306,305	309	2.1
309	Place Surcharge Material on Bldg Pad	10 days	Thu 6/27/13	Wed 7/10/13	308,307	310,314S	2.1
310	Surcharge wait time	40 days	Thu 7/11/13	Wed 9/4/13	309	311	2.1
311	Remove Excess Surcharge Material	5 days	Thu 9/5/13	Wed 9/11/13	310	312,373	2.1
312	Bldg Pad Complete	0 days	Wed 9/11/13	Wed 9/11/13	311	373	Mile
328	**Water & Fire Mains**	**14 days**	**Fri 8/23/13**	**Wed 9/11/13**			
329	Make Water Main Tap	1 day	Fri 8/23/13	Fri 8/23/13	326,88	332	2.1
332	Make Fire Main Tap	1 day	Mon 8/26/13	Mon 8/26/13	329	330	2.1
330	Install Water Main/Backflow	5 days	Tue 8/27/13	Mon 9/2/13	332	333	2.1
333	Install Fire Main/Backflow	5 days	Tue 9/3/13	Mon 9/9/13	330	331	2.1

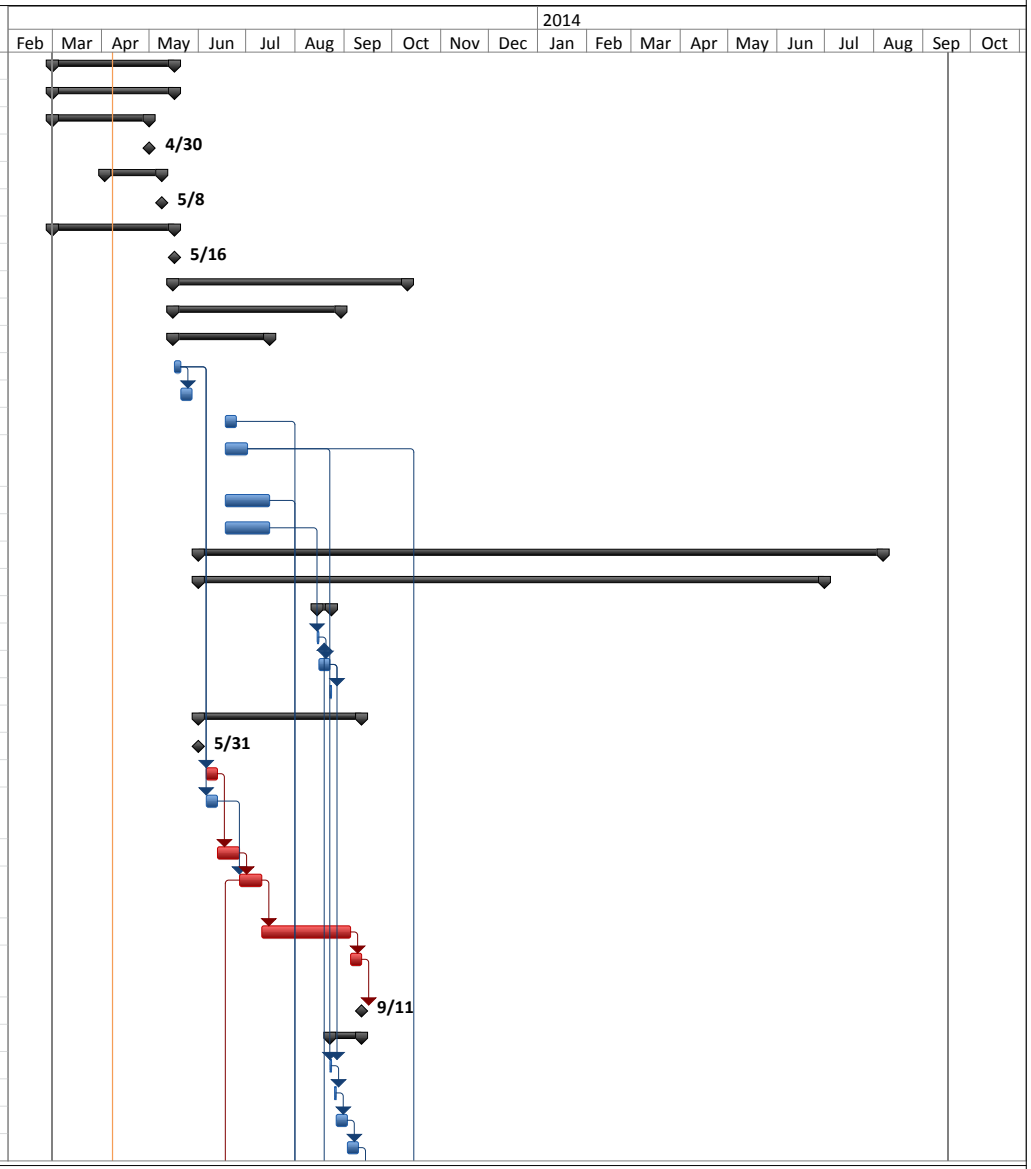

Project: East Roswell Library Mast
Date: Mon 4/8/13

Task | External Tasks | Manual Task | Finish-only | Baseline Milestone
Split | External Milestone | Duration-only | Deadline | Baseline Summary
Milestone | Inactive Task | Manual Summary Rollup | Critical | Progress
Summary | Inactive Milestone | Manual Summary | Critical Split
Project Summary | Inactive Summary | Start-only | Baseline

East Roswell Library
Bid Package Schedule

ID	Task Name	Duration	Early Start	Early Finish	Predeces	Successor	Text1
331	Put WM in Service	1 day	Tue 9/10/13	Tue 9/10/13	333	334	2.1
334	Put FM in Service	1 day	Wed 9/11/13	Wed 9/11/13	331	776	2.1
344	**Site Retaining Walls**	**140 days**	**Thu 8/29/13**	**Wed 3/12/14**			
345	Construct South Retaining Wall	20 days	Thu 8/29/13	Wed 9/25/13	320	346	2.1
347	**Parking Lots**	**21 days**	**Thu 4/10/14**	**Thu 5/8/14**			
348	Finish Grade Lots	5 days	Thu 4/10/14	Wed 4/16/14	341	349	2.1
349	Subgrade/Base	5 days	Thu 4/17/14	Wed 4/23/14	348	350	2.1
350	Curb & Gutter	5 days	Thu 4/24/14	Wed 4/30/14	349	351	2.1
351	First Lift Paving	3 days	Thu 5/1/14	Mon 5/5/14	350	352,315	2.1
352	Final Lift Paving	3 days	Tue 5/6/14	Thu 5/8/14	351	368	2.1
313	**Site Grading**	**228 days**	**Thu 6/27/13**	**Mon 5/12/14**			
314	Rough Grade Site (Cut/Fill)	20 days	Thu 6/27/13	Wed 7/24/13	309SS	317,336	2.1
315	Finish Grade Site	5 days	Tue 5/6/14	Mon 5/12/14	351	354,355	2.1
353	**Site Hardscaping**	**25 days**	**Tue 5/13/14**	**Mon 6/16/14**			
354	Sidewalks	5 days	Tue 5/13/14	Mon 5/19/14	315	363,342,:	2.1
356	Steel Edge Containment at Overhang	5 days	Tue 6/3/14	Mon 6/9/14	363	361	2.1
361	Gravel under Overhang	2 days	Tue 6/10/14	Wed 6/11/14	356	368,367	2.1
316	**Stormwater System**	**235 days**	**Thu 7/25/13**	**Wed 6/18/14**			
317	Temp Entrance Drive	2 days	Thu 7/25/13	Fri 7/26/13	314	318	2.1
318	Divert/Demo Existing Stormwater Line	3 days	Mon 7/29/13	Wed 7/31/13	317	319	2.1
319	Install SW Piping/Structures/Headwall	10 days	Thu 8/1/13	Wed 8/14/13	318,85,3	320,325	2.1
320	Install/Protect SW Detention Systems	10 days	Thu 8/15/13	Wed 8/28/13	319	321,345	2.1
321	Install/Protect Infiltration Areas	5 days	Thu 8/29/13	Wed 9/4/13	320	322	2.1
322	Install Rip Rap Dissipator	3 days	Thu 9/5/13	Mon 9/9/13	321	323	2.1
323	Remove Protection/Put in Service	2 days	Tue 6/17/14	Wed 6/18/14	367,322	369	2.1
366	**Site General**	**10 days**	**Mon 6/16/14**	**Mon 6/30/14**			
367	Site Construction Complete	0 days	Mon 6/16/14	Mon 6/16/14	365,361	323	Mile
369	Work off deficiency List	5 days	Tue 6/24/14	Mon 6/30/14	368,323	798	All
370	**Building Construction**	**225 days**	**Thu 9/12/13**	**Wed 7/23/14**			
371	**Structure**	**62 days**	**Thu 9/12/13**	**Fri 12/6/13**			
372	**Basement/Overhang**	**36 days**	**Thu 9/12/13**	**Thu 10/31/13**			
386	Underslab Fire Protection	3 days	Tue 10/15/13	Thu 10/17/13	377,88	380	2.1
422	**Main Level Low Roof Area North**	**50 days**	**Thu 9/26/13**	**Wed 12/4/13**			
429	Underdrain at Foundation	1 day	Mon 11/18/13	Mon 11/18/13	428	430	2.1
430	Geofabric/Porous Fill at Underdrain	3 days	Tue 11/19/13	Thu 11/21/13	428,183	431SS	2.1
405	**Main Level High Roof Area**	**56 days**	**Thu 9/19/13**	**Thu 12/5/13**			

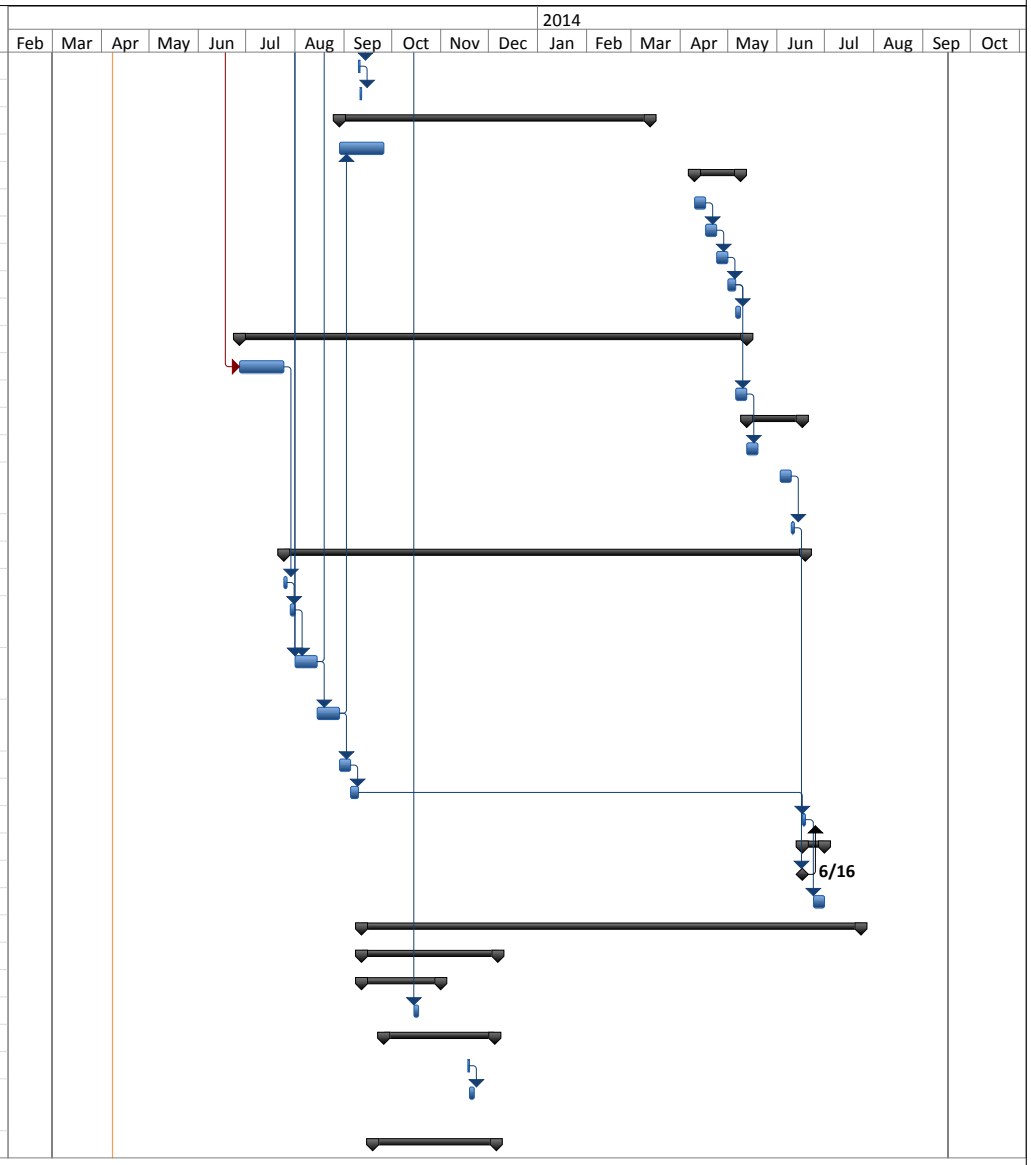

Project: East Roswell Library Mast
Date: Mon 4/8/13

Task	External Tasks	Manual Task	Finish-only	Baseline Milestone
Split	External Milestone	Duration-only	Deadline	Baseline Summary
Milestone	Inactive Task	Manual Summary Rollup	Critical	Progress
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Baseline	

East Roswell Library
Bid Package Schedule

ID	Task Name	Duration	Early Start	Early Finish	Predeces	Successor	Text1
421	Underdrain at Foundation	1 day	Fri 11/8/13	Fri 11/8/13	420	411	2.1
411	Geofabric/Porous Fill at Underdrain	4 days	Mon 11/11/13	Thu 11/14/13	410,421	412SS	2.1
440	**Main Level Low Roof Area East**	**51 days**	**Fri 9/27/13**	**Fri 12/6/13**			
446	Underdrain at Foundation	1 day	Mon 11/18/13	Mon 11/18/13	445	447	2.1
447	Geofabric/Porous Fill at Underdrain	3 days	Tue 11/19/13	Thu 11/21/13	446	448SS	2.1
472	**Exterior Skin**	**101 days**	**Fri 11/8/13**	**Fri 3/28/14**			
572	**West Elevation**	**60 days**	**Fri 11/8/13**	**Thu 1/30/14**			
588	Basement Dry-in	0 days	Fri 12/27/13	Fri 12/27/13	418,586	651	Mile
607	**Roof**	**87 days**	**Fri 11/8/13**	**Mon 3/10/14**	**203**		
625	**Stairwell Roof**	**65 days**	**Mon 11/25/...**	**Fri 2/21/14**			
629	Stairwell Dry In	0 days	Fri 2/21/14	Fri 2/21/14	628,571	680	Mile
618	**Low Roof East**	**72 days**	**Wed 11/20/...**	**Thu 2/27/14**			
622	Main Roof Field Dry-in	0 days	Mon 1/6/14	Mon 1/6/14	621	623	Mile
623	Building Complete Dry-in	0 days	Thu 2/27/14	Thu 2/27/14	621,497	693,752,	Mile
636	**Roofing General**	**7 days**	**Fri 2/28/14**	**Mon 3/10/14**			
638	Work off deficiency List	5 days	Tue 3/4/14	Mon 3/10/14	637	798	All
603	**Exterior Skin General**	**14 days**	**Mon 3/10/14**	**Fri 3/28/14**	**185**		
604	Exterior Skin Complete	0 days	Mon 3/10/14	Mon 3/10/14	600,571	605	Mile
606	Work off deficiency List	10 days	Mon 3/17/14	Fri 3/28/14	605,202	798	All
457	**Bridge**	**52 days**	**Mon 2/3/14**	**Tue 4/15/14**			
469	Bridge Complete	0 days	Fri 4/4/14	Fri 4/4/14	464	470	Mile
471	Work off deficiency List	5 days	Wed 4/9/14	Tue 4/15/14	470	798	All
639	**Interior Construction**	**189 days**	**Fri 11/1/13**	**Wed 7/23/14**			
676	**Stairwell**	**54 days**	**Mon 1/13/14**	**Thu 3/27/14**			
689	Work off deficiency List	5 days	Fri 3/21/14	Thu 3/27/14	688	798	All
640	**Basement**	**107 days**	**Fri 11/1/13**	**Mon 3/31/14**			
665	Bldg Permanent Power	0 days	Tue 1/21/14	Tue 1/21/14	664,662	671,670,	Mile
675	Work Off Deficiency List	5 days	Mon 2/3/14	Fri 2/7/14	674	798	All
666	Start-Up HVAC	0 days	Mon 3/31/14	Mon 3/31/14	709,779	780,781,	Mile
751	**Main Level Non-Access Flooring Area**	**96 days**	**Tue 1/7/14**	**Tue 5/20/14**			
796	Work off deficiency List	10 days	Wed 5/7/14	Tue 5/20/14	795,195	798	All
690	**Main Level Access Flooring Area**	**153 days**	**Mon 12/23/...**	**Wed 7/23/14**			
712	Access Floor Installed	0 days	Fri 3/21/14	Fri 3/21/14	711	713	Mile
750	Work off deficiency List	8 days	Mon 7/14/14	Wed 7/23/14	749	798	All
797	**Project General**	**10 days**	**Wed 7/23/14**	**Wed 8/6/14**			
801	**Closeout Phase**	**66 days**	**Tue 6/17/14**	**Tue 9/16/14**			
803	Test & Balance	15 days	Tue 6/17/14	Mon 7/7/14	735	804	All
813	Submit Closeout Documentation	20 days	Tue 6/17/14	Mon 7/14/14	735	814	All

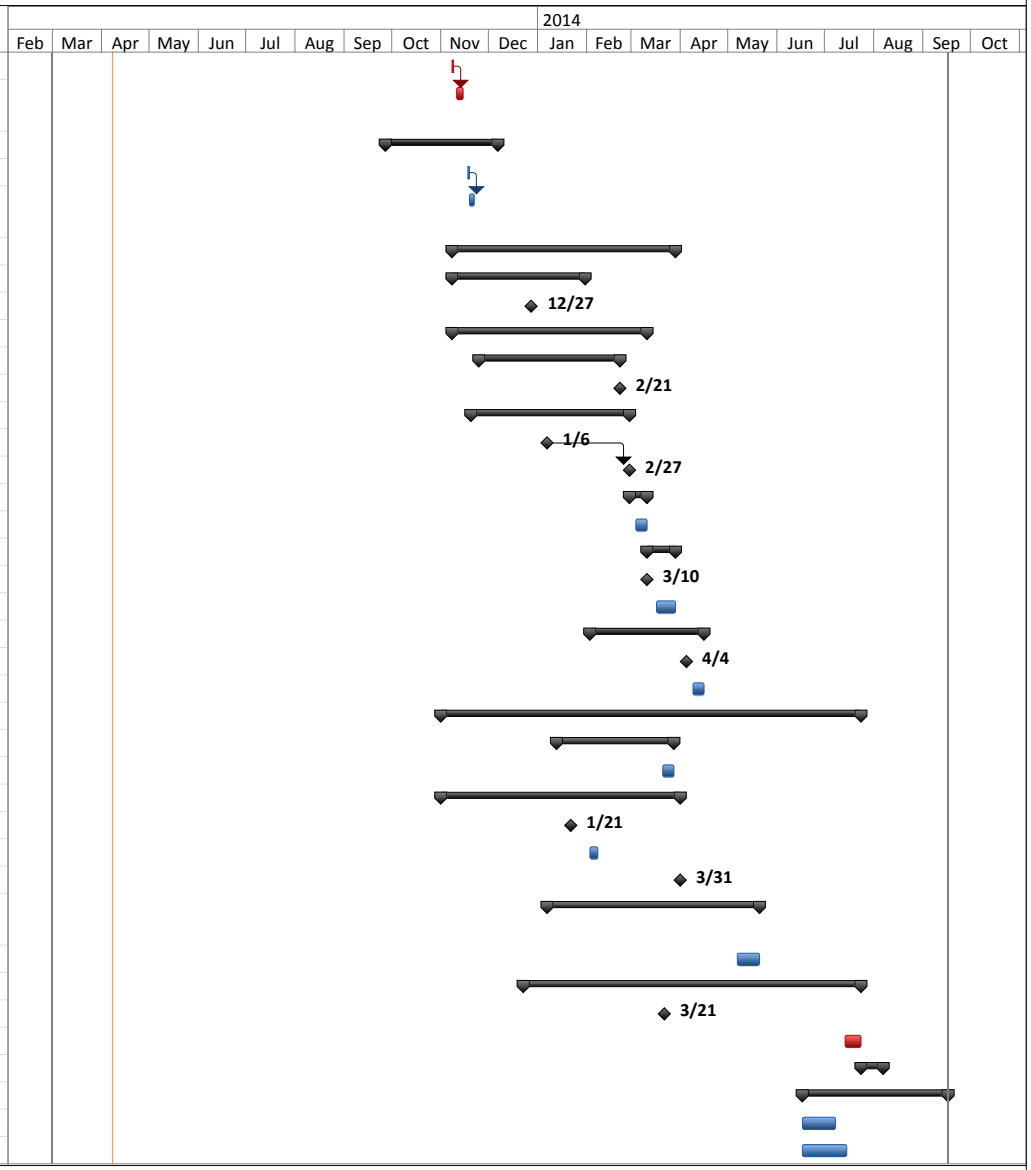

Project: East Roswell Library Mast
Date: Mon 4/8/13

Task | External Tasks | Manual Task | Finish-only | Baseline Milestone
Split | External Milestone | Duration-only | Deadline | Baseline Summary
Milestone | Inactive Task | Manual Summary Rollup | Critical | Progress
Summary | Inactive Milestone | Manual Summary | Critical Split
Project Summary | Inactive Summary | Start-only | Baseline

East Roswell Library
Bid Package Schedule

ID	Task Name	Duration	Early Start	Early Finish	Predeces	Successor	Text1
805	Substantial Completion	0 days	Mon 8/11/14	Mon 8/11/14	804,802	806,807,8	Mile
815	Work off Punchlists	18 days	Fri 8/15/14	Tue 9/9/14	806,807	816	All
816	Final Completion	0 days	Tue 9/9/14	Tue 9/9/14	812,815	817	Mile
818	Grand Opening	0 days	Tue 9/16/14	Tue 9/16/14	817		Mile



Project: East Roswell Library Mast
Date: Mon 4/8/13

Task	External Tasks	Manual Task	Finish-only	Baseline Milestone
Split	External Milestone	Duration-only	Deadline	Baseline Summary
Milestone	Inactive Task	Manual Summary Rollup	Critical	Progress
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Baseline	

SUBCONTRACT AGREEMENT
WITH
AJAX BUILDING CORPORATION OF GEORGIA

Georgia License #GCCO 002625 / GCQA 002638

SUBCONTRACTOR:_____ SUBCONTRACT #:_____

PHYSICAL ADDRESS:_____

CITY, STATE, & ZIP CODE: _____ PO BOX ADDRESS: _____

TELEPHONE NO: _____ FAX NUMBER: _____ CONTACT NAME: _____

SUBCONTRACT SUM: _____

COST CODE(S): _____

VENDOR #: _____ PROJECT #: _____

PROJECT NAME: _____

PROJECT ADDRESS: _____

THIS AGREEMENT is made this 1st day of January, 2013 by and between AJAX BUILDING CORPORATION OF GEORGIA, 1080 Commerce Blvd., Midway, FL. 32343, ("Contractor") and _____ _____ ("Subcontractor").

For the consideration hereinafter named, Subcontractor covenants and agrees with Contractor as follows:

1. DEFINITIONS
   a. The term "Subcontractor's Work" shall mean the work, labor, services, materials, and all items required to be done and furnished by Subcontractor under this Subcontract which is a portion of the entire work (hereinafter "Work") required of Contractor by the Contract Documents, as defined below.
   b. The term "Owner" shall mean the person, entity, partnership, firm, corporation, municipality, county, or department or agency of the State or Federal government directly contracting with Contractor for the performance of the Work.
   c. The terms "Architect/Engineer" shall mean the Architect or Engineer identified as such in the prime contract between Owner and Contractor.
   d. The terms "Building" or "Structure" or "Project" shall mean the building, structure, or project defined by and in the Contract Documents, which shall also include outside utilities, sidewalks, landscaping, roads, streets, and other subjects and objects of construction provided for in the Contract Documents.
   e. The "Owner" is Fulton County, a political subdivision of the State of Georgia of Georgia, and where appropriate shall include the representatives and agents of Owner including the Architect/Engineer.
   f. The term "Contractor" shall include Contractor and its surety, if any, notwithstanding that specific reference to Contractor or surety may be contained in some provisions of this Subcontract and not in others.
   g. The term "Subcontractor" shall include Subcontractor and all of its lower tier subcontractors, suppliers, vendors, and any other person or entity for whom it may be liable.
   h. Whenever the term "including" is used, the same shall mean including but not limited to.
   i. Words used in this Subcontract in the masculine gender include the feminine and neuter, the singular includes the plural and the plural, the singular.

2. SUBCONTRACTOR'S WORK
   a. Subcontractor agrees to provide all work required to complete and will complete the following described items of Subcontractor's Work in connection with the construction of the Project and will furnish all management, supervision, labor, materials, scaffolding, equipment, systems machinery, tools, apparatus, transportation, all required shop drawings, all required samples, machinery, plant, services, engineering and testing incident thereto or as are usually performed or furnished in connection with such Subcontractor's Work whether or not specifically mentioned or shown, but generally included under this class of craft or trade contract or fairly implied therein as necessary for the satisfactory completion of the WORK and shall, as often as directed by Contractor, completely clean all Subcontractor's Work and remove all contributing debris from the job site or to locations designated by Contractor and perform all work necessary to complete the items of Subcontractor's Work as stated herein and as described in Attachment "A" attached hereto and made a part hereof. All Subcontractor's Work shall be of good workmanship and installed to provide a complete system where

applicable. Subcontractor also represents and acknowledges that at the time of entering into this Subcontract, no substitution of any materials or equipment was contemplated by Subcontractor in establishing the Subcontract Sum, except as may be specifically recited in this Subcontract.

b. Subcontractor shall be bound to Contractor by the terms of this Subcontract and the Contract Documents. To the extent of Subcontractor's Work, Subcontractor shall assume toward Contractor all the obligations and responsibilities which Contractor by the Contract Documents assumes toward Owner, except for those provisions relating to payment or requirements for payment of subcontractors for the Work, which are specifically excluded. Subcontractor acknowledges its opportunity to inspect the Contract Documents prior to signing this Subcontract. Subcontractor shall include in its agreements with lower tier subcontractors contracting to perform any portion of Subcontractor's Work, a provision by which, to the extent of its portion of Subcontractor's Work , the lower tier subcontractor shall be bound to Subcontractor to the same extent Subcontractor is bound to Contractor herein, and by which the lower tier subcontractor shall assume all of the obligations and responsibilities to Subcontractor which Subcontractor assumes to Contractor under this Subcontract and the Contract Documents.

c. Before undertaking each part of Subcontractor's Work, Subcontractor shall carefully study and compare the Contract Documents which pertain to that part of such work, including all pertinent figures and dimensions, to all applicable field measurements. Subcontractor shall promptly report in writing to Contractor any error, omission, or conflict which Subcontractor may discover within or between the Contract Documents and the field measurements, and shall obtain a written interpretation or clarification from Contractor before proceeding with any affected Subcontractor's Work. In the event of a conflict within the Contract Documents, the higher standard or greater requirement shall prevail, unless governed otherwise by the Contract Documents. Unless provided to the contrary in the Contract Documents, Subcontractor shall not be liable to Owner, Contractor, Architect/Engineer for any error, omission, conflict, or inconsistency in the Contract Documents, unless Subcontractor had actual knowledge, or in the exercise of reasonable care should reasonably have known of them, or prepared such Contract Documents, and failed to report same to Contractor.

d. In the event Subcontractor performed any Subcontractor's Work prior to the execution of this Subcontract, all of the rights and liabilities of the parties for the performance of such work are expressly merged and included within and shall be governed by the terms of this Subcontract, all compensation due Subcontractor for such work is expressly included in the Subcontract Sum set forth herein, and Contractor shall have no obligation or liability to Subcontractor for such work separate and apart from the terms of this Subcontract.

3. CONTRACT DOCUMENTS

a. Contract Documents consist of the Agreement between Contractor and Owner, including all documents attached or referenced therein, all Conditions of the Contract between Contractor and Owner (General, Supplementary and Other Conditions), the drawings, the specifications and all addenda issued prior to the execution of the Agreement, and all subsequent modifications, as provided in Paragraph 9. The payment provisions and any requirements for payment of subcontractors between Owner and Contractor are specifically excluded from the Contract Documents incorporated in this Subcontract. Terms defined in the Contract Documents shall have the same definition when used in this Subcontract, unless the context clearly requires otherwise.

b. Except as modified by this Subcontract, Subcontractor's Work shall be performed and completed in accordance with the Contract Documents, including addenda, if any.

c. The Contract Documents, including the agreement, drawings, plans, specifications, conditions, and addenda, shall be kept on file in the office of Contractor (although certain confidential and proprietary information therein may be redacted), and shall be considered as exhibits to this Subcontract. Work shown on the drawings but not specified, or specified but not shown on the drawings, shall be performed under this Subcontract. Drawings and specifications are to be construed as supplementing each other.

d. Should Owner not engage an Architect/Engineer on the Project, the rights of the parties shall be determined without necessity of any certificate, determinations, or other function to be performed by an architect or engineer.

e. Contractor makes no representation that the plans and specifications or any addenda are free of errors or omissions, and Subcontractor acknowledges that it has reviewed all of the plans and specifications and any addenda; that it has independently determined that the plans, specifications and addenda are adequate for purposes of determining the WORK and the Subcontract Sum, and that it agrees with the methods, sequence, procedures and details shown in the plans and specifications and any addenda.

4. SUBMITTALS

a. The term "submittals" as used in this Subcontract shall include those shop drawings which are specially prepared by Subcontractor or any of its subcontractors, manufacturers, suppliers or distributors and which are required by the Contract Documents to be submitted to Contractor for submission to the Owner, Architect/Engineer, or others to illustrate some portion of Subcontractor's Work, including showing in detail: (1) the proposed fabrication and assembly of structural elements; and (2) the installation including form, fit and attachment details of materials or equipment. The term "submittals" shall also include shop schematics; fabrication drawings; coordination drawings; diagrams; layouts; descriptive literature; illustrations; schedules; product, performance and test data; templates; tests; samples; together with any and all other materials or data related to the materials, methods, and equipment used or proposed for use in the

performance of this Subcontract. Contractor and Owner may duplicate, use, and disclose in any manner and for any purpose any submittals furnished under this Subcontract. Samples are physical examples which illustrate materials, equipment or workmanship and establish standards by which Subcontractor's Work will be judged.

b. Time is of the essence in the performance of this Subcontract. Subcontractor shall proceed at once to prepare the shop drawings and other required submittal data, and it shall furnish same and await approval by or on behalf of Owner prior to fabrication of any item to be furnished under this Subcontract. Submittal data shall be prompt and complete to insure scheduled delivery of such equipment and/or materials, so as not to delay the progress of either Subcontractor's Work or the remaining Work required of Contractor pursuant to its contract with Owner. Adequate copies of such submittals shall be submitted, plus the number of copies desired by Subcontractor for its use. In the instance of specifically prepared fabrication drawings, the submittal shall consist of one reproducible drawing and at least four prints. Subcontractor agrees to keep Contractor fully informed regarding its delivery schedule and will immediately advise Contractor should any delay be anticipated. A complete, up-to-date procurement schedule will be submitted on forms acceptable to Contractor, upon request. Procurement schedule and construction schedule shall be compatible.

c. A daily record of salient job matters shall be maintained and recorded by Subcontractor as applicable to Subcontractor's Work and shall be submitted weekly to Contractor. Submittal of such records shall be a condition precedent to any obligation to make progress payments under this Subcontract. Contractor's receipt and review of such records shall in no event be deemed an admission or a presumption that any statement therein is accurate and without dispute.

d. Approval of any shop drawing or submittal shall not relieve Subcontractor of any duty and responsibility to perform Subcontractor's Work in the manner necessary to produce the results required by the Contract Documents. No portion of Subcontractor's Work requiring submission of a shop drawing or other submittal shall be commenced until the submittal has been approved by or on behalf of Owner. Any Subcontractor's Work done by Subcontractor before approval of the applicable submittals shall be at Subcontractor's sole risk. All such portions of Subcontractor's Work shall be in accordance with approved submittals.

e. Subcontractor shall prepare, review, approve and submit to Contractor within the earlier of the time required by the Contract Documents or ten (10) days after the date of this Subcontract, all required submittals in sufficient form, number and in such sequence as to cause no delay, disruption or interference in Subcontractor's Work or in the work of Contractor, any other contractor, any subcontractors or Owner's own forces. When required by the Contract Documents, Subcontractor shall also obtain approval of all machinery and equipment to be incorporated into Subcontractor's Work. When requesting approval, Subcontractor shall furnish to Contractor the name of the manufacturer, model number and other required information concerning the performance, capacity, nature and rating of the machinery and other equipment.

f. By providing submittals, Subcontractor represents to Owner, Contractor, and Architect/Engineer that it has coordinated all such submittals, reviewed them for accuracy and completeness as well as compliance with this Subcontract and the Contract Documents, and determined and verified all related materials, field measurements, and field construction criteria, or will do so, and that it has checked and coordinated the information contained within such submittals with the requirements of Subcontractor's Work and of the Contract Documents. Submittals submitted to Contractor without evidence of such Subcontractor's approval may be returned for resubmission.

g. If any submittal contains any deviation from the requirements of this Subcontract or the Contract Documents, Subcontractor shall describe such deviation in writing separate from the submittal or on resubmitted submittals, to be furnished at the time of submission to Contractor. If Owner or its authorized representative approves any such variation, Contractor shall transmit an appropriate Change Order, except that if the deviation is minor or does not involve any equitable adjustment to the Subcontract Sum or extension of the time(s) for completion of Subcontractor's performance, a Change Order need not be issued. Subcontractor shall not be relieved of responsibility for any deviation from the requirements of this Subcontract or the Contract Documents by Contractor's forwarding any submittals for approval. In addition, no transmittal or approval of any of the foregoing by Contractor, Owner, or Architect/Engineer shall under any circumstances: alter the requirements of this Subcontract for quality, quantity, finish, design and configuration; constitute acceptance of any method, material or equipment not ultimately acceptable to Owner; relieve Subcontractor from responsibility for any errors or omissions in such submittals; or relieve Subcontractor from responsibility for complying with the requirements of this Subcontract or the Contract Documents, except with respect to deviations described and approved pursuant to this section.

h. Subcontractor shall bear all costs and expenses associated with the preparation and approval of all submittals together with field measuring, sampling, and shipping or delivery connected with any of the foregoing. Subcontractor further agrees that the entire cost and expense of altering, reworking and refinishing any manufactured or fabricated items not conforming to approved submittals shall be borne by Subcontractor.

i. The term "substitution" shall mean any substitution for, modification of or deviation from the requirements of this Subcontract, the Contract Documents or any approved submittals with respect to any materials, equipment and methods of construction or manufacture applicable to Subcontractor's Work herein.

j. Subcontractor shall make no substitutions without prior written approval of Contractor and Owner. No approval will be given by Contractor unless applied for in writing by Subcontractor setting forth a full disclosure of the effect of the proposed substitution upon the Work of Contractor, any other contractors, any subcontractors and Owner's own forces, and approval thereof is given by Owner.

k. If Subcontractor shall make any unauthorized change in Subcontractor's Work either through submittals or actual field work, it shall be solely responsible for the aesthetics as well as the structural and functional adequacy and acceptance thereof by Owner. Any rejection by reason of aesthetics or any structural or functional inadequacies which may develop because of such change shall be remedied by Subcontractor at its sole cost and expense, despite any approvals that may be given by Owner, unless such change is specifically approved and included in a Change Order.

l. All costs and expenses of any additional work and the redoing or repairing of any other work of Subcontractor's, Contractor's, any other contractor's, any subcontractor's or Owner's own forces, resulting from such substitution shall be borne by Subcontractor, and Subcontractor shall promptly reimburse Contractor for the entire cost and expense suffered or incurred by Contractor or others.

5. SUPERINTENDENCE

a. Subcontractor shall provide adequate, competent, and experienced full-time, on-site supervision (satisfactory to Contractor) during the performance of Subcontractor's Work. Such supervision shall have the authority to carry out directions from Contractor relating to such work or responsibility and shall have the authority to make decisions binding on Subcontractor.

b. Subcontractor shall provide technical services as required to affect the operation of equipment and/or material furnished under this Subcontract, including performance of specific testing, if any, and shall instruct Owner's personnel in the operation, maintenance and control of such equipment.

6. MATERIAL AND WORKMANSHIP

a. All Subcontractor's Work shall be done to the final approval of Contractor, Architect/Engineer, and Owner, and their decision as to the performance of Subcontractor's Work in accordance with the plans and specifications and the true meaning of the plans and specifications shall be final, subject only to the limits stated in the Contract Documents.

b. Subcontractor shall provide safe and sufficient facilities at all times for inspection of Subcontractor's Work by Contractor, Architect/Engineer, and Owner or their authorized representatives.

c. Should Contractor, Architect/Engineer, or Owner condemn or fail to approve any work or materials to be furnished under this Subcontract, Subcontractor shall within 24 hours after receiving written notice from Contractor of such determination, proceed promptly to take down all portions of the unapproved work and remove from the grounds and buildings all materials whether worked or unworked, which are subjected to condemnation or disapproval, and shall promptly make good all such work and all other work damaged or destroyed in removing or making good said condemned work.

d. Subcontractor shall conform to and abide by any additional specifications, drawings, or explanations furnished by the Architect/Engineer to illustrate Subcontractor's Work, subject to the provisions of Article 9.

7. PROGRESS AND COMPLETION

a. Unless otherwise provided herein, Subcontractor shall begin Subcontractor's Work as soon as the Project is ready for such work, or immediately upon verbal or written notice by Contractor, and shall carry on said work efficiently and at a rate that will not cause delay in the progress of the work of Contractor, or any other subcontractor, contractor, or Owner's own forces. Subcontractor shall cooperate with Contractor in the scheduling and performance of Subcontractor's Work, so as to avoid delay, disruption or interference with the work of Contractor, any other subcontractor, contractor, or Owner's own forces.

b. Subcontractor shall at all times, supply and promptly pay for, adequate tools, appliances, equipment, a sufficient number of properly skilled workmen, and a sufficient amount of materials and supplies of specified quality to efficiently and properly prosecute Subcontractor's Work in accordance with Contractor's schedule, and any modifications thereto, in order to achieve a project completion date established by Contractor with due consideration that other work is dependent upon Subcontractor's Work for proper and timely completion.

c. Subcontractor is to employ workmen who will work in harmony with those employed by Contractor and other subcontractors, contractors, and Owner's own forces,. Should the work of Contractor, or any other subcontractor be stopped, or materially delayed, in the judgment of Contractor, due to Subcontractor's not complying with this Paragraph, then Contractor shall have the right, in addition to any and all other rights provided in this Subcontract, after forty-eight (48) hours written notice to Subcontractor, to employ other subcontractors or workers to supplement or complete the requirements of this Subcontract in conformance with this Paragraph, in which event the cost to supplement or complete Subcontractor's Work shall be charged to Subcontractor.

d. It is further understood that contracts will be awarded and labor employed upon the job without discrimination as to whether the employees of any contractor or subcontractor are members or are non-members of any labor organization. Subcontractor agrees that in the event of a work stoppage resulting from a labor dispute directed at Subcontractor, Contractor shall have the right to proceed as set forth herein, including employing such workers as Contractor deems appropriate to complete the requirements of this Subcontract and the cost thereof shall be charged to Subcontractor.

e. If, in the opinion of Contractor, Subcontractor falls behind in the progress of Subcontractor's Work, Contractor may, upon forty-eight (48) hours written notice, direct Subcontractor to take such steps as Contractor deems necessary to regain the progress of Subcontractor's Work, including requiring Subcontractor to increase the labor force, number of shifts, overtime operations, days of work, amount of plant or other remedies, and to submit for approval a schedule

demonstrating the method under which the required rate of progress will be regained, without additional costs to Contractor. Contractor may, upon reasonable notice, require Subcontractor to prosecute in preference to other parts of Subcontractor's Work, such parts of Subcontractor's Work as Contractor may require. Contractor may employ such workers and purchase and lease such materials and equipment as Contractor deems necessary in order to regain the proper rate of progress with respect to Subcontractor's Work. All costs incurred by Contractor in so regaining the progress of Subcontractor's Work shall be charged to Subcontractor.

f. In the event Subcontractor fails to meet the requirements of the schedule and is unable to regain lost time, Contractor shall have the right to accelerate other trades work and any additional cost thereof shall be charged to Subcontractor.

g. In performing this Subcontract, Subcontractor agrees that it will not discriminate against any employee or applicant for employment because of race, color, national origin, sex, religion or handicap (or sexual orientation to the extent required by applicable law) in the manufacture, assembly, delivery, erection and installation of materials and performance of Subcontractor's Work covered by this Subcontract.

8. MUTUAL RESPONSIBILITY

a. The quantity and scope of Subcontractor's Work is directed by the whole of the Contract Documents, and Subcontractor acknowledges its obligation under this Subcontract to coordinate Subcontractor's Work with materials and equipment to be furnished by others to ensure a completely compatible system. Accordingly, Subcontractor shall review the fabrication drawings and the product data of all items requiring integration and compatibility with Subcontractor's Work.

b. Subcontractor shall review the surfaces provided by others to which Subcontractor's Work is to be applied, and shall notify Contractor of any known defect or condition detrimental to proper procedures, prior to the commencement of Subcontractor's Work; otherwise, commencement of such work will be deemed Subcontractor's acceptance of the conditions of such surfaces.

c. Subcontractor shall: (1) provide continuous and effective protection at all times for Subcontractor's Work, materials, supplies and equipment furnished under this Subcontract as well as the work, materials, supplies, equipment and property of Contractor, any other subcontractors, contractors or Owner's own forces, protecting the same from damage or injury as a result of Subcontractor's operations under this Subcontract; (2) report promptly to Contractor, in writing, any damage to such work, materials, supplies, equipment or property of others, describing fully such occurrence and damage including wherever available, an estimate of the cost and expense of restoration and identification of the affected party or parties; (3) bear and be solely liable for any and all loss and damage of any kind prior to the final completion and acceptance of Subcontractor's Work, unless such loss or damage is caused solely by the negligence of Contractor and is subject to recovery under any applicable insurance policies as may be in effect; and (4) promptly reimburse Contractor for the entire cost and expense suffered or incurred by Contractor in correcting or curing any delay, disruption, interference or damage, including the cost and expense of repairing, replacing, refinishing or restoring any such damaged work, materials, equipment or property and administrative time. When it is necessary to cross curbs, sidewalks or other improvements Subcontractor shall protect them from damage. Subcontractor shall repair or pay for the repair of any damaged curbs, sidewalks or other improvements.

d. Contractor shall make available within reasonable limits, temporary services for the benefit of Subcontractor, consisting of sanitary toilet facilities, potable water (drinking water and cups provided by Subcontractor), 110 volt electric service at the building and litter containers. Litter containers shall not be utilized for the deposit of scrap or waste construction materials. Subcontractor shall constantly maintain proper housekeeping controls of construction debris and litter arising from its operations and shall clean on a daily basis, all debris and foreign material attributable to its operation.

e. Subcontractor will provide, maintain and remove from the Project site, on completion of Subcontractor's Work, all its temporary offices, structures for the use of its employees, sheds and storage facilities, together with all utilities, electric, gas, telephone and water. Storage areas for the use of Subcontractor shall be designated by Contractor, and no materials or equipment shall be stored by Subcontractor except in areas approved by Contractor. Such storage areas shall be maintained in an orderly condition by Subcontractor. Storage within the building is prohibited unless authorized in writing by Contractor.

f. Subcontractor shall be responsible for all hazardous waste materials created or released as a result of the performance of Subcontractor's Work. Subcontractor shall create approved storage containment areas for temporary storage and remove from the site at its expense as required by D.E.P. (or other applicable agency). Subcontractor shall maintain evidence of proper disposal including manifests and provide copies to Contractor. This provision shall remain in effect regardless of who is responsible for construction debris removal.

g. Subcontractor shall provide and be responsible for layout and its accuracy as is necessary for the performance of Subcontractor's Work.

h. Subcontractor shall perform all cutting, fitting, patching, sleeving, grouting, and sealing of Subcontractor's Work that may be required to fit it to, receive, or be received by the work of others as shown, or reasonably implied by the Contract Documents; or as required, or reasonably implied by the rules and regulations, codes, and requirements of all regulatory agencies having jurisdiction over the Project; or as required or reasonably implied to achieve consistency and compatibility with the design of elements being penetrated.

i. Subcontractor shall pay to Contractor the reasonable value for the use of any of Contractor's equipment which Contractor may permit Subcontractor to use.

j. Anchoring devices required for Subcontractor's Work to be built into concrete or masonry shall be furnished by Subcontractor with accompanying location drawings. All anchoring devices will be installed by Subcontractor unless otherwise agreed to by the parties.

k. Temporary lighting, heat or ventilation required to perform Subcontractor's Work is the responsibility of Subcontractor.

l. Subcontractor represents that it has investigated, examined, inspected, and thoroughly familiarized itself with the Contract Documents, the site and adjoining premises in connection with which Subcontractor's Work is to be performed, that it has thoroughly informed itself as to any difficulties in connection with performing Subcontractor's Work, and that Contractor has made no representation of any kind or nature not contained in this Subcontract. Commencement of Subcontractor's Work or any portion thereof, by Subcontractor shall be conclusive evidence that the job site, or that part at which such work is being installed, is in proper condition for the reception and installation of Subcontractor's Work. Before commencing Subcontractor's Work, Subcontractor will satisfy itself as to the location of all utilities that may affect or interfere with such work. Subcontractor will fully protect all utilities, and keep them operating at all times.

9. CHANGES

a. In the event Contractor requests Subcontractor to review a proposed modification to the Project which may affect Subcontractor's Work, Subcontractor shall respond in writing within seven (7) days after receipt of such request, or other reasonable time limits as the parties may agree, stating the effect of the proposed modification upon its performance, including details of cost and time effects thereof. Otherwise, Subcontractor shall accept the determination of Contractor as to the effect of the proposed modification or change.

b. Contractor may at any time, without notice to the Surety of this Subcontract, by written order designated or indicated to be a change order, make any change in Subcontractor's Work within the general scope of this Subcontract. Upon receipt of any Change Order, Subcontractor shall promptly proceed with the work involved, which shall be performed under the applicable terms and conditions of this Subcontract and the Contract Documents, except as may otherwise be specifically provided. Nothing shall excuse Subcontractor from proceeding promptly with the prosecution of the work as ordered in such Change Order and failure or refusal to do so shall constitute a default of this Subcontract.

c. Additions to, or changes in this Subcontract shall be made only upon written order, approved by Contractor. A Change Order or Contract Amendment signed by Subcontractor shall be final and binding upon Subcontractor as a full and complete adjustment for the change(s) made, including the equitable adjustment to the Subcontract Sum and extension(s) of the time for completion of Subcontractor's performance. Should the parties be unable to agree as to the value of such work to be added or omitted, Subcontractor shall proceed under the written order of Contractor, from which order the stated value of the work shall be omitted. The value of such work shall be determined in accordance with the following paragraph.

d. In the event Subcontractor is required by Contractor to perform additional work for which the amount of compensation is not previously agreed upon, Subcontractor shall prepare and submit to Contractor a proposal describing the estimated quantities and cost involved. Subcontractor shall keep accurate, detailed and itemized records of the costs of any such change and shall report such costs to Contractor in the form and manner prescribed by Contractor. Subcontractor shall, if requested, furnish each day to Contractor, certified copies of all time sheets, receiving and inspection reports and all other basic documents required by Contractor, to evidence the expenditures of Subcontractor as a result of such change. Subcontractor's application to Contractor for payment shall be accompanied by certified copies of all pertinent payrolls, invoices, and vouchers relating to the additional work. Contractor's or Owner's receipt, or acknowledgment of Subcontractor's change order claims, or any other alleged claim, or any notice or report, including reports of cost and time, or any payments made, shall not be construed as Contractor's or Owner's acknowledgment, or acceptance of the accuracy and validity of any portion, until such time as a change order is fully executed.

e. Unless specifically stated otherwise in the Contract Documents, for any change, the increase in the Subcontract Sum will be the total of direct labor costs marked up at the rate of _____% for payroll burden and direct labor and material costs marked up 5% for profit, and 5% for overhead. Material costs subject to mark-up are defined as those items which become a permanent part of Subcontractor's Work. Direct labor costs subject to mark-up are defined as the direct wages of field personnel from foreman down, required to put Subcontractor's Work in place. All other costs including bonds and insurance will be included in the allowable mark-ups shown above. Any reductions in the Subcontract Sum shall be calculated in the same manner.

f. Subcontractor will provide to Contractor an itemization and sufficient documentation of labor and material to adequately support increases or reductions in the Subcontract Sum.

g. Receipt by Contractor of payment from Owner for changed or extra work ordered or directed by Owner shall be a condition precedent to the right of Subcontractor to receive payment from Contractor, and the liability of Contractor's surety, if any, shall be subject to the same condition precedent.

10. DELAYS

a. No interruption, interference, inefficiency, suspension or delay in the commencement or progress of Subcontractor's Work for any cause whatever, including those for which Owner, Architect/Engineer, or Contractor may be responsible, in whole or in part, shall relieve Subcontractor of its duty to perform or give rise to any rights, damages or additional compensation from Contractor to Subcontractor. Subcontractor's sole remedy against Contractor as result thereof shall be the right to seek an extension to the time fixed for the completion of Subcontractor's Work in accordance with paragraph

10c. This paragraph applies to claims for early completion, as well as to claims for late completion. Notwithstanding anything in this paragraph to the contrary, Subcontractor may be compensated for interruptions, interferences, inefficiencies, suspensions or delays, not attributable to Subcontractor's fault or neglect, to the extent, and only to the extent, Contractor is able to recover and collect the same from Owner or others. Collection of these sums is an absolute condition precedent to any obligation of Contractor to pay Subcontractor for such claims.

b. Subcontractor shall reimburse Contractor for the entire cost and expense suffered or incurred for all liquidated or actual delay damages assessed by Owner against Contractor, all actual costs, expenses and damages suffered or incurred by Contractor including Contractor's job overhead for the period of time of such delay, disruption or interference, all damages suffered or incurred by any other contractor or subcontractor on the Project for which Contractor may be liable, including Contractor's administrative costs and attorney's fees, resulting in any manner whatsoever, directly or indirectly, from any and all delays, disruptions and interferences caused by Subcontractor. The fact that liquidated or other delay damages may have been specified by Owner in the Contract Documents shall not operate as a limitation on Subcontractor's liability to Contractor for delay damages. In the event any such damages are caused by Subcontractor and another person or entity, Contractor shall have the right to reasonably apportion such damages between the parties, and such apportionment shall be final and binding upon Subcontractor. Subcontractor further agrees that neither the payment of such damages nor any liability suffered or incurred for the payment of such damages shall release Subcontractor from its obligation to otherwise fully perform this Subcontract.

c. Should Subcontractor be delayed in the prosecution of Subcontractor's Work by any act, neglect or default attributable to Contractor, Architect/Engineer, or Owner or by any damage caused by fire, lightning, earthquake, hurricane, or any other cause for which Subcontractor is not responsible, either in whole or in part, then the time fixed for the completion of Subcontractor's Work pursuant to the terms of this Subcontract shall be extended for a period equivalent to the time lost by reason of such causes. However, no time extension shall become operative unless a notice of claim is presented in writing to Contractor within seventy-two (72) hours of the first occurrence of the delay and such claim is subsequently approved in writing by Contractor. Subcontractor agrees that such extension of time for completing Subcontractor's Work precludes, satisfies and cancels any and all other claims Subcontractor may have against Contractor on account of such delay. Permitting Subcontractor to continue after the time to complete Subcontractor's Work has expired, shall not be construed as a waiver by Contractor of any claims for loss or damage for breach by Subcontractor of one or more of the provisions of this Subcontract.

11. DEFAULT AND TERMINATION

a. If Subcontractor at any time shall refuse or neglect to supply sufficient properly skilled workers or materials or equipment of the proper quality and quantity, or fail in any respect to prosecute Subcontractor's Work with promptness and diligence, or cause by any action or omission the stoppage or interference with work of Contractor or other subcontractors, or fail in the performance of any of the requirements contained in this Subcontract, or be unable to meet its debts as they mature, Contractor may, at its option, send Subcontractor written notice of such default. If Subcontractor fails to cure the default within seventy-two (72) hours of the sending of the notice of default, Contractor may terminate this Subcontract by sending written notice of termination to Subcontractor. Thereafter, Contractor may take possession of the materials, tools, appliances and equipment of Subcontractor at the Project site, and through itself or others provide labor, equipment and materials to prosecute Subcontractor's Work, on such terms and conditions as shall be deemed necessary by Contractor, and shall deduct the cost, including all charges, expenses, losses, costs, damages and attorneys' fees, incurred as a result of Subcontractor's failure to perform, from any money then due or to become due to Subcontractor. If Contractor so terminates Subcontractor, Subcontractor shall not be entitled to any further payments under this Subcontract until Subcontractor's Work has been completed and accepted by Contractor, Architect/Engineer, and Owner, and payment has been received by Contractor from Owner. In the event that the unpaid Subcontract Sum exceeds Contractor's cost of completion, the difference shall be paid to Subcontractor after the expiration of all applicable warranties; but if such expense exceeds the balance due, Subcontractor shall promptly pay the difference to Contractor.

b. Contractor shall have the right to terminate this Subcontract, by written notice, without Subcontractor being at fault, for any cause or for its own or Owner's convenience and require Subcontractor to immediately stop work. In such event, Contractor shall pay Subcontractor for that portion of Subcontractor's Work actually performed in an amount proportionate to the total Subcontract Sum. Contractor shall not be liable to Subcontractor for any other costs nor for prospective profits on any portion of Subcontractor's Work not performed. However, if the reason for the termination is any action or default by Owner, or as a result of court order or public authority, then Contractor shall be liable to Subcontractor only for any greater sum which Contractor receives from Owner with respect to Subcontractor's Work, less any costs, credits, set-offs, and backcharges incurred by Contractor.

c. Subcontractor shall have the right to terminate this Subcontract only after it has provided Contractor with a written notice of default. Contractor shall have twenty days (20) to commence the cure of any default. In the event that Contractor fails to cure any default for which it has been provided notice, then upon an additional ten (10) days notice, Subcontractor shall have the right to terminate this Subcontract.

d. The remedies of Contractor provided for in this paragraph and in any part of the Contract Documents shall be cumulative, and not exclusive, of all other remedies which Contractor may have for breach of this Subcontract by Subcontractor, or as a result of Subcontractor's failure to perform any of the requirements of this Subcontract. Subcontractor and its surety

shall be liable for all losses, damages, and expenses, including administrative time and attorneys' fees in the prosecution or defense of any action, arbitration, trial or appeal, enforcement of any judgment, bankruptcy or insolvency proceedings, or any subsequent proceedings or appeals from any order or judgment entered therein, incurred by or resulting to Contractor arising out of any breach of this Subcontract.

e. If Subcontractor fails to clean-up and dispose of all trash and waste materials created by Subcontractor, within eight (8) hours of receipt of written notice to Subcontractor's field supervisor, Contractor shall have the right to perform such clean-up for Subcontractor and Subcontractor shall pay Contractor Thirty ($ 30.00) dollars per man hour plus transportation and dumping costs to perform the clean-up. Clean-up of Subcontractor's Work and the daily removal of debris from the areas of the WORK is mandatory. Each day, all trash and debris is to be removed to a location acceptable to Contractor. Fire exits, corridors and doorways shall be kept clear of debris and open to pedestrian and wheelchair traffic at all times, specifically including nights and weekends. Unless agreed to otherwise, Subcontractor shall remove all trash and debris resulting from Subcontractor's work from the site on a weekly basis.

12. CLAIMS AND DISPUTES

a. Subcontractor shall make all claims to Contractor for extras and extensions of time for which Owner may be responsible in the manner provided for in the Contract Documents, if any, for claims by Contractor upon Owner, and in sufficient time for Contractor to comply with the requirements of the Contract Documents for making such claims to Owner, but in no case more than seven (7) days from the initial occurrence of any event giving rise to such claim. Subcontractor shall be bound by the resolution of any dispute between Contractor and Owner involving any portion of Subcontractor's Work. Contractor shall be liable to Subcontractor only to the extent that Contractor actually recovers and collects from Owner for each claim or extra, less Contractor's cost associated with the claim or extra. If such costs cannot be determined, they shall be prorated among the parties involved. Subcontractor shall make all claims to Contractor for extras and extensions of time for which Contractor may be responsible within seven (7) days from the initial occurrence of any event giving rise to such claim. Failure to provide timely notice shall be a waiver of such claim.

b. Except as otherwise provided for in this Subcontract, any dispute arising under this Subcontract which is not resolved shall be decided by Contractor, who shall reduce its decision to writing and furnish a copy thereof to Subcontractor. The decision of Contractor shall be final and conclusive unless, within twenty (20) calendar days from the date of receipt of such decision, Subcontractor contests said decision in writing. Failure to contest Contractor's decision within this time limit will be a waiver of all further claims relating thereto. No claim, dispute or controversy between Owner and Contractor, or between Contractor and Subcontractor, shall be a basis to delay or suspend Subcontractor's Work or interfere with its progress or performance, unless directed otherwise by Contractor, and Subcontractor shall continue with all performance required by this Subcontract and shall proceed in accordance with all directives of Contractor. Failure to proceed shall constitute a default of this Subcontract, regardless of the ultimate decision on such claim, dispute or other controversy, and will be cause for termination of this Subcontract.

c. In the event Subcontractor is desirous of pursuing an appeal of an adverse final decision rendered by Owner, or the Architect/Engineer that affects Subcontractor's interests, and provided Contractor's interests are unaffected, Subcontractor shall bear the full cost and sole responsibility for prosecuting such appeal. Subcontractor shall continue to work and maintain the progress schedule, unless otherwise agreed to in writing by the parties.

d. At the option of Contractor, any and all unresolved disputes or controversies arising out of or relating to this Subcontract, or the breach thereof, whether of law, equity, or fact of any nature whatsoever, shall be decided by binding arbitration administered by the American Arbitration Association in accordance with its Construction Industry Arbitration Rules. Contractor reserves the right to object to any individual arbitrator who is employed by or affiliated with a competing organization. The arbitrator(s) shall have the power to decree any and all relief of an equitable nature, including but not limited to relief such as a temporary or a permanent injunction, and shall also have the power to award damages and costs. Any decree or award rendered by the arbitrator(s) may be entered in any court having jurisdiction. In no event may a demand for arbitration be made after the date on which a legal action concerning the matter in dispute would be barred by the appropriate statute of limitations. As a condition precedent to the filing or continuation of any arbitration demand, the parties shall engage in a good faith mediation of the dispute.

e. In the event the Contract Documents between Owner and Contractor provide for arbitration or other non-judicial proceeding as the forum for the resolution of disputes, and a claim, dispute or other controversy exists between Owner and Contractor which may involve Subcontractor, Subcontractor hereby expressly agrees, at the option of the Contractor to be joined as an additional party in any and all such arbitrations or other proceedings, or if a separate arbitration or other proceeding already exists or is separately initiated, Subcontractor expressly agrees to the consolidation of all such arbitration or other proceedings, it being the intent of Contractor to resolve all of the rights and obligations of all interested parties at one time in one forum rather than in multiple proceedings. If any claim, dispute or other controversy involving Subcontractor is prosecuted or defended by Contractor and Subcontractor is not directly a party or litigant in such proceeding, Subcontractor shall have the full responsibility for the preparation of all of its claims and defenses to claims asserted against it and shall bear all of its costs and expenses including all of its attorneys' fees and further, shall cooperate fully with Contractor and furnish all documents, statements, witnesses and other information required by Contractor for such purpose. Subcontractor shall promptly reimburse Contractor for the entire cost and expense incurred by Contractor including a proportionate share of Contractor's attorneys' fees and costs, to the extent of Subcontractor's

interest or involvement in such claim, dispute or other controversy.

f. This agreement to mediate and arbitrate shall not apply to any claim: (1) of contribution or indemnity asserted by one party to this Subcontract against the other party and arising out of an action brought in a state or federal court, or brought in arbitration by a person who is under no obligation to arbitrate the subject matter of such action with either of the parties hereto and who does not consent to such arbitration; (2) asserted by Subcontractor against Contractor if Contractor asserts said claim, either in whole or part, against Owner, and the Contract between Contractor and Owner does not provide for binding arbitration and Contractor and Owner do not subsequently agree to arbitration, or the Contract does so provide but the two arbitration proceedings cannot be consolidated; and (3) for punitive damages.

g. Any claim, dispute or other matter between Contractor and Subcontractor relating to this Subcontract shall be governed by the laws of the State of Georgia. Venue for any action arising out of this Subcontract shall be Fulton County, Georgia.

13. REGULATORY COMPLIANCE

a. Subcontractor's attention is directed to the compliance requirements of the Contract Documents. Subcontractor shall comply therewith as applicable. Specific references made, but not limited to:

1. Apprenticeship trainee requirements.
2. Equal opportunity employment requirements.
3. Special trade permits and connection permits or fees.
4. Compliance with employee wage rate determinations required by governing authorities and those specified within the Contract Documents.
5. Insurance provisions
6. Environmental controls.

b. Subcontractor shall comply with all applicable local, state and federal laws, codes, regulations and ordinances.

c. Subcontractor shall comply with the Williams-Steiger Occupational Safety and Health Act of 1970, and the General Safety Rules and Regulations of the Construction Industry as currently required by the governing authorities having jurisdiction thereof, and such other labor laws as may be applicable, and report immediately to Contractor any injury to any employee of Subcontractor at the site of the Project on the form attached as Attachment "B."

d. Subcontractor shall comply with the requirements of the Building Department, and comply with all other laws, ordinances and regulations, and save Contractor from all annoyances and fines arising out of Subcontractor's Work, and give proper authorities all requisite notices relating to Subcontractor's Work, and procure and pay for all necessary official licenses or permits to carry on Subcontractor's Work.

e. Compliance with all federal, state and local tax laws, social security laws, and unemployment compensation laws is required. In the event Subcontractor is not a resident in the State of Georgia, Subcontractor shall procure a Non-Resident Contractor's Bond and comply with all requirements of Sections 48-13-30 through 48-13-38 of the Official Code of Georgia Annotated, together with Rules and Regulations promulgated by the Commissioner of Revenue. All costs associated with providing such bond are included in the Subcontract Sum. Subcontractor shall provide a copy of such Bond to Contractor before Subcontractor's first request for payment on this Project. Notwithstanding anything to the contrary in this Subcontract, should Subcontractor fail to provide Contractor with such Bond, Contractor may withhold up to 4% of any sums otherwise due Subcontractor under this Subcontract, exclusive of retainage, until such time as Subcontractor furnishes Contractor with a certificate issued by the Commissioner of Revenue showing that all sales taxes accruing by reason of this Subcontract have been paid and satisfied

f. Material Safety Data Sheets (MSDS) are required on toxic materials that Subcontractor intends to use on the Project. Subcontractor shall furnish any required MSDS to Contractor, and thirty (30) days prior to delivery identify specifically any toxic material. Subcontractor shall meet the obligations of the Georgia Statutes to properly train and advise its employees, subcontractors, sub-subcontractors, agents and invitees. Failure by Subcontractor to comply with the preceding requirements shall constitute a material breach of this Subcontract, and any items or material delivered to the job site without complying with all of the foregoing shall be considered as non-conforming, and Contractor may reject and return it, or hold it at Subcontractor's expense.

g. In the event that the Project is a State-funded "Major Facility Project," as defined in OCGA §50-8-18 (2009) (effective July 1, 2010), as may be amended from time to time, Subcontractor shall comply with all policies, procedures, and standards adopted by the Department of Community Affairs relating to Subcontractor's Work, including without limitation purchasing and documenting the use of Georgia-based materials and products, participating in functional performance tests and verification of TAB reports, and any applicable commissioning activities.

h. In the event Owner is a public body, Subcontractor warrants to Contractor that Subcontractor: (1) has fully complied and shall continue to fully comply, at its own cost, with all applicable federal, state and local laws, ordinances, rules, and regulations governing immigration, including but not limited to the Immigration Reform and Control Act of 1986 ("IRCA"), as amended from time to time, and the Georgia Security & Immigration Compliance Act of 2006 ("GSIC"), as amended from time to time, along with their I-9 employer verification provisions; (2) has upon signing this Subcontract contemporaneously signed and returned to Contractor a Subcontractor Affidavit that strictly conforms to the requirements of Georgia Administrative Code §300-10-.08; (3) has properly trained and shall continue to properly train its staff regarding the execution and retention of I-9 employment verification forms; (4) is not now in violation of IRCA or GSIC;

(5) has provided written notification to Contractor of all prior citations by any government agency for violations of IRCA or GSIC; (6) has implemented and shall continue to implement a company-wide I-9 employment verification policy (including, but not limited to the use of the EEV/Basic Pilot for employment eligibility verification of all new hires where such usage is required by federal or state law);and (7) Subcontractor has and shall cause all lower-tier subcontractors to sign a Subcontractor Affidavit that Subcontract shall return to Contractor, and to comply with all other requirements of this provision. Subcontractor further warrants that should Subcontractor become aware of any government audit of its employees or employer verification procedures, it shall immediately notify Contractor in writing of such an audit and provide Contractor a copy of the findings when they are made available.

i. In the event of Subcontractor's violation of the above, Subcontractor shall bear all costs resulting from such violation and shall hold Contractor harmless from any damages (including attorneys' fees), claims, and causes of action arising from such violation.

14. INDEMNITY AND INSURANCE

a. Subcontractor shall, at its cost and expense, furnish and maintain: commercial general liability and property damage insurance; commercial automobile liability and property damage insurance; workers' compensation insurance and employer's liability insurance; coverage under the Longshoremen's and Harbor Worker's Act and the Jones Act, if applicable, together with such other insurance as may be required by the Contract Documents or by law. Such liability insurance shall include coverage for premises - operations (including explosion, collapse, and underground coverage), elevators, independent contractors, products and completed operations and blanket contractual liability on all written contracts, all including broad form property damage coverage. All coverages shall be written on an occurrence basis. Claims-made coverage is not acceptable. All coverages shall be maintained in full force and effect at all times during the term of this Subcontract from the date of commencement of Subcontractor's performance of any work and until expiration of the warranty period or such other date as may be established elsewhere in the Contract Documents, whichever is later. If any other coverages are required to be maintained after final payment, an additional certificate evidencing such coverage shall be submitted with Subcontractor's final Application for Payment. All such coverages shall be written by a company or companies satisfactory to Contractor, and include Contractor, Owner and Architect/Engineer as additional insureds. The coverage and limits of said insurance are set forth in Attachment "C" and Subcontractor shall provide Contractor with a certificate of insurance evidencing Subcontractor's compliance with this requirement with a 30 day notice of cancellation provision. Upon Contractor's request, Subcontractor shall supply Contractor with certified copies of all insurance policies required to be furnished by Subcontractor. In the event Subcontractor fails or neglects to obtain or renew the required insurance and furnish evidence thereof to Contractor with the executed Certificate of Insurance form, Contractor shall have: (a) the right, but not the obligation, to procure such insurance and charge the cost to Subcontractor; or (b) to deem such failure or neglect on the part of the Subcontractor as a default of this Subcontract. No payment of any portion of the Subcontract Sum shall be due to Subcontractor until the provisions of this section have been fully satisfied.

b. By execution of this Subcontract, Contractor and Subcontractor waive all rights against each other and any of Subcontractor's subcontractors, Owner, Architect/Engineer and of its consultants, any other contractors, and any other subcontractors, together with all of their agents and employees, for damages caused by fire or other perils to the extent covered by the builders risk property insurance, excepting such rights as they may have to any insurance proceeds. Subcontractor also waives all rights of subrogation against Contractor and Owner for loss of, or damage to Subcontractor's work, tools, machinery, equipment, material or supplies. Subcontractor shall include the same waiver of subrogation in all of its subcontracts for the Project. The foregoing waiver of subrogation shall be effective as to any person or entity even though that person or entity would otherwise have a duty to indemnify, did not directly or indirectly pay the insurance premium and whether or not the person or entity had an insurable interest in the property damaged.

c. The insurance specified above shall provide that said insurance is primary non-contributory coverage to any insurance that Contractor or Owner may carry.

d. To the fullest extent permitted by law, Subcontractor shall indemnify and hold harmless Contractor (including its affiliates, parents and subsidiaries), and the Owner, Architect/Engineer and all agents officers, directors and employees of any of them (the "Indemnitiees"), from and against any claim, damage, loss, cost, and expense, including but not limited to attorneys' fees, arising out of or resulting from the performance of Subcontractor's obligations herein, if attributable to (1) bodily injury, sickness, disease, or death or injury to persons or destruction of tangible property, including loss of use thereof, caused in whole or in part by any act or omission of Subcontractor or anyone directly or indirectly employed by Subcontractor or anyone for whose acts Subcontractor may be liable, unless resulting from such indemnified party's sole negligence; or (2) breach of any obligation under this Agreement by Subcontractor, or anyone directly or indirectly employed by Subcontractor or anyone for whose acts Subcontractor may be liable. In the event any employee of Subcontractor, anyone directly or indirectly employed by Subcontractor, or anyone for whose acts Subcontractor may be liable makes a claim against any Indemnitee, the indemnification obligations herein shall not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Subcontractor under workers' compensation acts, disability benefit acts, or other employee benefit acts. In addition to indemnifying and holding harmless the Indemnitees, Subcontractor shall, upon receiving written direction from any Indemnitee, promptly assume the defense of such claim, suit, arbitration or proceeding at Subcontractor's expense with counsel approved by such

Indemnitee. Contractor shall cooperate with Subcontractor in any such defense. If Subcontractor fails or refuses to promptly undertake the defense of such claim, suit, arbitration or proceeding after receiving a written request from any Indemnitee, or fails or refuses at any time to proceed with the defense to the satisfaction of the Indemnitee, Contractor may assume said defense at Subcontractor's expense. Subcontractor shall indemnify and hold harmless the Indemnitees from and against any claims involving the Subcontractor's nonpayment of its subcontractors, laborers, vendors, or materialmen. The obligations to indemnify shall survive the termination or completion of this Subcontract.

e. Subcontractor shall provide a performance bond and a labor and material payment bond, each in the amount of one hundred percent (100%) of the Subcontract Sum, on a form provided by Contractor and with a corporate surety authorized to do business in the State of Georgia and acceptable to Contractor, which bonds shall be furnished within seven (7) days of execution of this Subcontract. Subcontractor acknowledges that the cost of all bond premiums has been included in the Subcontract Sum. The surety hereby waives notice of any alteration or changes to this Subcontract and Subcontractor's Work . No payment of any portion of the Subcontract Sum shall be due to Subcontractor until the provisions of this section have been fully satisfied.

f. Commencement of Subcontractor's Work without having provided said bonds shall not be considered a waiver, or release by Contractor of the requirement for bonds, and Subcontractor shall have proceeded with Subcontractor's Work at its own risk and shall not be entitled to payment until such bonds are delivered to Contractor.

15. ENCUMBRANCES

a. Subcontractor shall turn Subcontractor's Work over to Contractor in good condition and free and clear of all claims, encumbrances, or other liens and shall protect and save harmless Contractor and Owner from all claims, encumbrances or liens growing out of the performance of this Subcontract. If any subcontractor, laborer, or supplier of Subcontractor, or any other person or entity directly or indirectly acting for or through Subcontractor files a claim of lien or bond claim against Contractor, its surety, if any, the Project, the property or any part or any improvements, or against any monies due or to become due from Owner to Contractor or from Contractor to Subcontractor, Subcontractor shall satisfy, remove or discharge such lien or claim at its own cost and expense by payment, bond or otherwise, within 15 days of the date of its assertion, irrespective of any defense that Subcontractor may have to such claim of lien or bond claim. If Subcontractor shall fail or refuse to do so, Contractor shall have the right, in addition to any other rights and remedies provided by this Subcontract or by law, to satisfy, remove, or discharge the same by whatever means Contractor chooses, and Subcontractor shall promptly reimburse Contractor for the entire cost and expense suffered or incurred by Contractor. The provisions of this section shall not impose any duty or obligation upon Contractor to determine or adjust any disputes or claims between Subcontractor and any such claimant or to withhold any money for its protection.

b. Subcontractor shall, as often as requested by Owner or Contractor, furnish a sworn statement showing all parties who furnish labor or materials to Subcontractor, with their names and addresses and amounts due or to become due each of them.

c. Subcontractor shall furnish Contractor, if requested, evidence of the payment of all bills and expenses incurred by Subcontractor for labor, services, equipment and materials used by Subcontractor, and liability incurred by Subcontractor in any way for the purpose of using the same on or about the Project, and written releases, in form as provided by Contractor, from all persons, firms, or corporations that may have furnished to Subcontractor, any services, equipment and materials, whether on, or for the Project, and written releases of lien and/or bonds from all persons, firms and corporations that may have in any way had any dealing and agreements in connection with Subcontractor's Work.

d. Any and all transportation tax, sales tax, use tax or any other tax that might accrue through purchase of materials or amounts paid for labor by Subcontractor or occasioned by performance of this Subcontract are included in the Subcontract Sum. Any and all tax exemptions shall belong to Contractor and/or the Owner.

e. Subcontractor agrees that any payment due or that may come due is not assignable and that no part of this Subcontract can be assigned, except with the written consent of Contractor. Any assignment in violation of this provision shall be void and unenforceable

16. WARRANTIES

a. Subcontractor warrants to Contractor, Architect/Engineer, and Owner that all materials and equipment furnished shall be new unless otherwise specified, and that all Subcontractor's Work shall be of good quality, free from faults and defects and in conformance with the Contract Documents.

b. Subcontractor agrees to promptly make good, without cost to Contractor or Owner, any and all defects due to faulty workmanship or materials which may appear within the guarantee or warranty period(s) established in the Contract Documents, and if no such period(s) be stipulated in the Contract Documents, then such guarantee shall be for a period of one (1) year from the date of completion and acceptance of the Project by Owner. Subcontractor further agrees to execute any special guarantees as provided by the Contract Documents or required by law. Subcontractor shall require similar guarantees from all vendors and lower tier subcontractors.

c. Subcontractor agrees that the warranty period of equipment utilized for completion of the Project shall remain in effect for the entire warranty period from the date of Owner acceptance.

d. Subcontractor shall pay for all changes to Subcontractor's Work or the Work resulting from defects in Subcontractor's workmanship or materials, as well as, all expenses necessary to replace or repair either the Subcontractor's Work or the Work, including that damaged or disturbed by making replacements or repairs. This guarantee is in addition to all other guarantees, warranties and rights contained in the Contract Documents.

17. SPECIAL PROVISIONS

a. Unless otherwise stated, work hours are from 7:00 a.m. to 3:30 p.m., Monday through Friday. Holidays will be:

New Years Day	Memorial Day
Fourth of July	Labor Day
Thanksgiving Day	Day after Thanksgiving
Christmas Day	

Any work beyond these hours must have prior approval by Contractor's Project Manager or Superintendent.

b. Materials delivered to the job site shall be received, unloaded and stored by Subcontractor. All deliveries shall be coordinated with Contractor.

c. Subcontractor's special attention is called to Attachment "B" - "Project Safety Manual" which is to be strictly observed and rigidly enforced by Subcontractor during the performance of Subcontractor's Work.

d. Subcontractor shall be represented by person, or persons authorized to represent Subcontractor at weekly Safety and Subcontractor Meetings, commencing two weeks prior to the start date of Subcontractor's Work.

e. As-built documents and data shall be maintained and recorded by Subcontractor as applicable to Subcontractor's Work and may be reviewed monthly by Contractor, concurrently with Subcontractor's request for progress payments. Completion of accurate as-built documents is a condition precedent to receiving payment each month and at final completion.

f. Subcontractor shall bear all costs of testing. Where testing agency standards are referenced, all materials shall be tested and certified by an approved, independent testing company.

g. Location of employee parking, equipment parking, material storage, and temporary trailers will be subject to approval by Contractor.

h. Subcontractor will provide a list of suppliers prior to the first pay request.

i. A condition precedent to Subcontractor receiving progress payments is the delivery by Subcontractor to Contractor each month (regardless of whether any Subcontractor's Work was performed) of waivers of lien or waivers of right to claim against bond as required from Subcontractor and all sub-subcontractors and suppliers who have filed Notices to Contractor. Forms for use in this connection will be supplied by Contractor.

j. Signs shall not be posted by Subcontractor unless approved in writing by Contractor.

18. PAYMENTS

a. Subcontractor shall submit within ten (10) days of execution of this Subcontract and prior to any payment being made, a schedule of values with respective quantities illustrated, in accordance with the divisions of the Uniform Construction Index (UCI) or as required in the Contract Documents, if different. Unless otherwise directed, each allocation to a work item shall include the proportionate share of overhead and profit. The schedule of values must be acceptable to Contractor as to form and substance. Subcontractor shall show labor and material values independently.

b. It is expressly agreed that time is of the essence in the performance of this Subcontract. It is further expressly agreed that, any provision of the Contract Documents to the contrary notwithstanding, Subcontractor agrees that Contractor shall be under no obligation to pay Subcontractor for any work performed or materials or equipment furnished for this Project unless and until Contractor has been paid therefore by Owner, and the making of any and all progress and final payments and the amounts thereof are expressly subject to this absolute condition precedent. Subcontractor states that it relies primarily on the credit and ability of Owner to pay and not upon Contractor's credit or ability, and further, expressly accepts the risk that it will not be paid for Subcontractor's Work performed by it in the event that Contractor, for whatever reason, is not paid by Owner for such work. Subcontractor further agrees that the liability of Contractor's surety, if any, shall be subject to the same condition precedent.

c. Contractor agrees to pay Subcontractor for Subcontractor's Work the sum of _____ _____ _____ ($) ("Subcontract Sum").

The Subcontract Sum shall be paid by Contractor to Subcontractor as follows:

1. As Subcontractor's Work progresses, an amount equal to ninety percent (90%) of the value of completed Subcontractor's Work done from month to month, including the materials which are intended to be incorporated in the Project and which are properly stored on the site and meeting the requirements of the Contract Documents and certified by the Architect/Engineer or Owner.

2. On or before the twentieth day of each month (or such other day as Contractor may stipulate) Subcontractor shall submit to Contractor, a written and itemized Application for Payment based upon the approved schedule of values and representing a true and accurate estimate of the portion of Subcontractor's Work completed as of the date indicated in the Application for Payment and when permitted, an accurate inventory of materials and equipment suitably stored on the job site or other agreed upon location, reflecting the appropriate retainage and less previous payments, which Application for Payment shall be certified by an officer or representative of Subcontractor in a manner acceptable to Contractor, notarized and supported by valid lien waivers as set forth

elsewhere in this Subcontract or the Contract Documents, together with such additional documentation, invoices, vouchers, waivers, certifications and affidavits substantiating Subcontractor's right to payment as Contractor may request or the Contract Documents require. The form of Application for Payment shall be as furnished by Contractor. All Applications for Payment shall be subject to correction including revision to any prior or following Application(s) for Payment. Should any defective work, materials or equipment be discovered during the progress of construction, or should reasonable doubt arise as to whether certain work, materials or equipment is in accordance with this Subcontract or the Contract Documents, the value of such defective or questioned work, material or equipment shall not be included in any Application for Payment, or if previously included and paid, shall be deducted by Subcontractor in its next Application for Payment. It shall be Subcontractor's sole responsibility to submit each Application for Payment in the time and in the manner prescribed and on the form provided or approved by Contractor for such purpose, and in no instance shall Contractor be obligated to make any payment upon any Application for Payment not in compliance. Subcontractor agrees that any Application for Payment not in compliance may, at the option of Contractor, be held over for processing at the beginning of the month or other designated period next following correction, resubmission or late submission of such Application for Payment, without notice to Subcontractor.

3. Payment for stored materials shall be made as stipulated by the Contract Documents, and such requests for payments for stored materials shall be accompanied by vendor invoices, itemizing respective quantities and unit costs of such stored material and any other requirements of the Contract Documents. At its option, Contractor may make payment for stored material by joint check to Subcontractor and vendor and require, as a condition precedent to payment for stored materials, proper insurance and a waiver of lien or waiver of bond rights, effective as of the date of the payment. Material stored on the site, for which payment is requested, shall be in the care and custody of Subcontractor, and shall not be removed from the site without the written consent of Contractor. Payment to Contractor by Owner is an absolute condition precedent to the obligation of Contractor to pay Subcontractor for stored materials.

4. Final payment will be made within 20 days after Subcontractor has submitted its final Application for Payment and all required closeout documents together with any required certificates of insurance for any insurance coverages required to be maintained after the date of final payment and Contractor has received from Owner written acceptance together with payment in full for the Work. Final payment is further subject to Contractor's determination that all of the terms, conditions, requirements and covenants of this Subcontract have been well and truly met and discharged by Subcontractor. Acceptance of final payment by Subcontractor releases Owner, and Contractor and its surety from any and all claims arising out of or related to this Subcontract.

d. If at any time there shall be evidence of lien or claim for which, if established, Owner or Contractor or its surety might become liable, and which is chargeable to Subcontractor, or if Subcontractor shall incur any liability to Contractor, or Contractor shall have any claim or demand against Subcontractor of any kind or for any reason, whether or not reduced to judgment or award, Contractor shall have the right to retain out of any payment due, or to become due under this Subcontract or any other contract between Contractor and Subcontractor, an amount sufficient to compensate Contractor for and fully satisfy such liability, claim, or demand, and charge or deduct all cost of defense, or collection with respect thereto, including attorneys' fees. Should any claim or lien develop for which retained sums are insufficient or after all payments are made, Subcontractor shall pay to Contractor all monies that the latter may be compelled to pay in discharging such claims or liens or costs incurred in collecting said monies from Subcontractor.

e. No progress payment under this Subcontract shall be conclusive evidence of the performance of this Subcontract either in whole or in part, and no payment shall be construed to be acceptance of defective Subcontractor's Work or improper materials.

f. Subcontractor shall pay for all materials and labor used in connection with the performance of this Subcontract through the period covered by previous payments received from Contractor. Subcontractor shall accompany all Applications for Payment with its own lien and bond waiver for the period of time covered by its current Application for Payment, and with lien and bond waivers from all of its subcontractors, suppliers and others for the period of time covered by the previous Application for Payment and who may be entitled to assert a lien or bond claim on the Project. All lien and bond waivers shall be on a form provided by or approved by Contractor. Subcontractor is advised that no exceptions to this provision will be made and any Application for Payment not accompanied by proper lien and bond waivers will be cause for not processing the Application for Payment and withholding of payment. Contractor reserves the right, in its sole discretion, to make any payment to Subcontractor through checks made payable to the joint order of Subcontractor and such of Subcontractor's subcontractors, suppliers or any of Subcontractor's other creditors having potential rights or claims against the Project or any proceeds.

g. Final payment is further subject to Contractor's prior receipt from Subcontractor of all as-built drawings, certifications, maintenance manuals, operating instructions, written guarantees and warranties and bonds relating to the WORK, a final waiver of lien and bond, complete releases and an affidavit certifying Subcontractor's payment in full for all items relating to Subcontractor's Work.

h. All estimates and quantity calculations made by Owner or Architect/Engineer as to the weights, quantities and amount(s) of materials furnished and Subcontractor's Work shall be final and binding upon Subcontractor, and shall conclusively establish the amount(s) of materials furnished and Subcontractor's Work. It is understood and agreed that Subcontractor

shall receive no compensation for any materials furnished or Subcontractor's Work performed by it which is not approved and accepted by Owner and Architect/Engineer, and will make no claim against Contractor or its surety for any compensation based upon any estimate or quantity calculations other than those made by Owner or Architect/Engineer; provided, however, if Subcontractor, pursuant to any written directive of Contractor, furnishes any additional material or performs any additional work not provided for in the Contract Documents, Subcontractor will be compensated as provided in the Subcontract.

i. All payments due and unpaid under this Subcontract shall bear interest from the date payment was due at the rate of _0_____% per annum or, if not specified, at the legal rate of interest set forth in OCGA § 7-4-2(a)(1)(A).

j. Contractor may deduct from any amounts due or to become due to Subcontractor under this Subcontract or any other agreement between Contractor and Subcontractor any sums owed Contractor under this Subcontract or any other agreement between Contractor and Subcontractor.

k. The interest rates, periods of payment, conditions of payment, rights and remedies set forth in the Subcontract are intended to govern over any different or additional terms set forth in OCGA §§ 13-11-1, et seq.

19. MISCELLANEOUS

a. This Subcontract constitutes the entire and integrated agreement between Contractor and Subcontractor, and supersedes all prior negotiations, representations, understandings and agreements, either written or oral. Contractor shall not be liable in any way for any understandings or representations made by any of its representatives or agents prior to the execution of this Subcontract, unless such understandings or representations by Contractor are expressly stated in this Subcontract. This Subcontract may be amended only by written instrument signed by both Contractor and Subcontractor. No person acting for or on behalf of Contractor shall have authority to waive the requirement that all amendments and modifications to this Subcontract be in a writing signed by an authorized representative of Contractor.

b. Should any provision of this Subcontract be determined by a court to be unenforceable, such a determination shall not affect the validity and enforceability of any other section or part.

c. The failure of Contractor to enforce, at any time or any period of time, any one or more of the provisions of the Contract Documents shall not be construed to be and shall not be a waiver of any such provision or provisions or of its right thereafter to enforce each and every such provision.

d. Nothing contained in this Subcontract shall be deemed to create any contractual or third party beneficiary relationship between any parties other than Contractor and Subcontractor.

e. The headings provided in this Subcontract are for ease of reference only. The headings form no part of this Subcontract between the parties and shall be given no weight in the interpretation or construction of this Subcontract.

f. Except as may be provided in the Contract Documents, Subcontractor shall pay all royalties and licensing fees which may be due in connection with the WORK and shall defend all actions or claims against Contractor or Owner for such royalty or licensing fees and shall be liable to Contractor for any losses or damages as a result.

g. Contractor and Subcontractor for themselves, their successors, personal representatives and assigns, hereby agree to the full performance of the covenants of this Subcontract.

h. If this Subcontract is not duly and properly executed by Subcontractor and returned to Contractor within seven (7) days of its date, it is deemed withdrawn by Contractor.

IN WITNESS WHEREOF, Contractor and Subcontractor have signed this Subcontract the day and year first written above.

WITNESS

_____

WITNESS

_____

AJAX BUILDING CORPORATION OF GEORGIA

BY: _____

NAME/TITLE:

TYPE SUBCONTRACTOR NAME IN CAPS HERE

BY: _____

NAME/TITLE: _____
